



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	8						
							S	N	Half 1, 2019			Half 2, 2019	
									J	M	M	J	S
1		Harbour (G+25)	787 days	Mon 12/3/18	Mon 12/6/21								
2		Piling Work	217 days	Mon 12/3/18	Mon 9/30/19								
3		Sub-Structure upto Ground floor	110 days	Tue 10/1/19	Mon 3/2/20	2							
4		Super Structure	280 days	Tue 3/3/20	Mon 3/29/21	3							
5		Finishing	400 days	Tue 5/26/20	Mon 12/6/21	4SS+60 days							
6													
7		Glacier (G+25)	670 days	Tue 10/22/19	Mon 5/16/22								
8		Piling Work	100 days	Tue 10/22/19	Mon 3/9/20	2FS+15 days							
9		Sub-Structure upto Ground floor	110 days	Tue 3/10/20	Mon 8/10/20	8							
10		Super Structure	280 days	Tue 8/11/20	Mon 9/6/21	9							
11		Finishing	400 days	Tue 11/3/20	Mon 5/16/22	10SS+60 days							



Project: msproj11 Date: Sat 9/14/19	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Progress	
	Project Summary		Duration-only		Manual Progress	
	External Tasks		Manual Summary Rollup			
	External Milestone		Manual Summary			

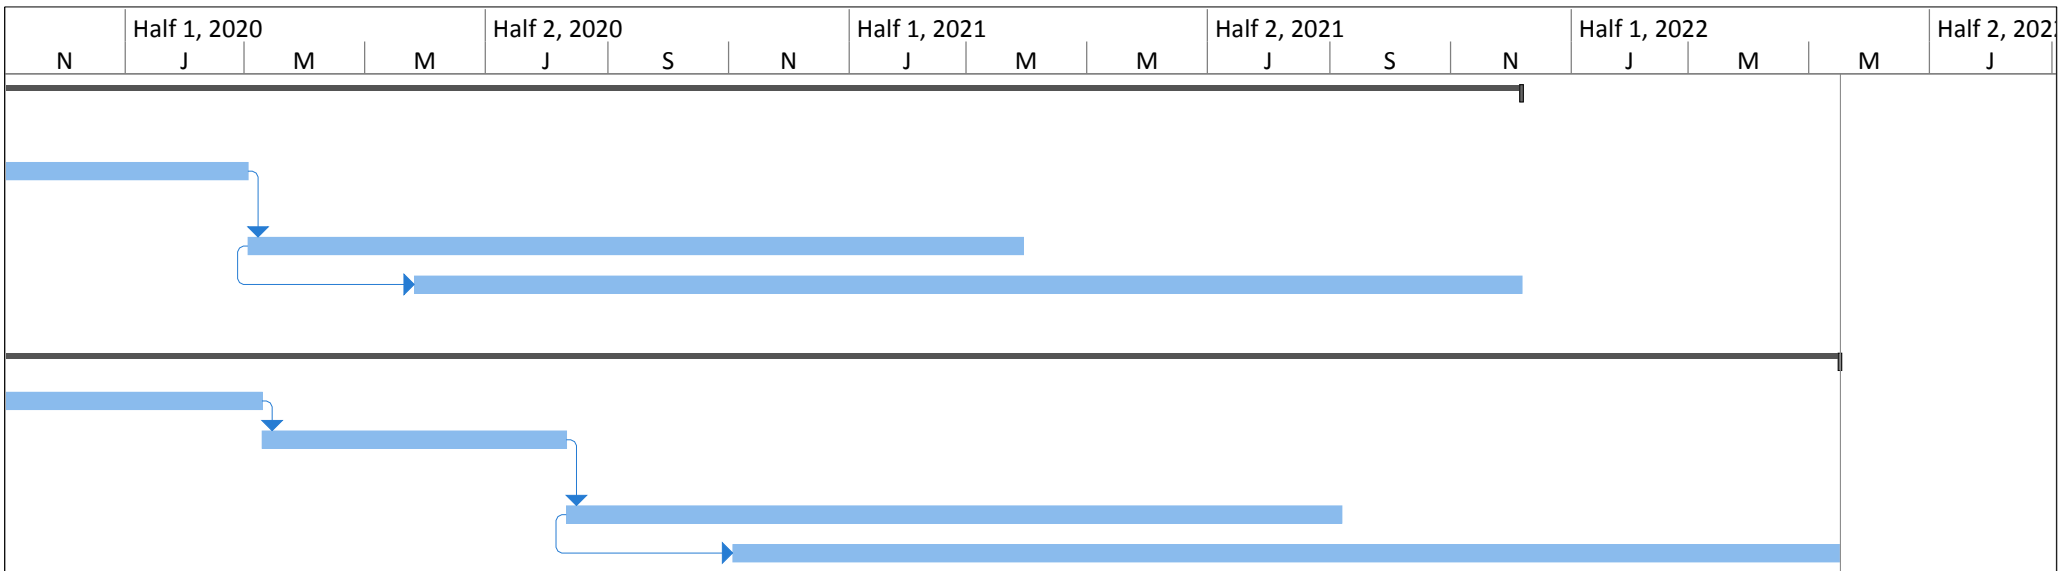

Project: msproj11
Date: Sat 9/14/19

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Progress	
Project Summary		Duration-only		Manual Progress	
External Tasks		Manual Summary Rollup			
External Milestone		Manual Summary			
