


ID	Task	Task Name	Duration	Start	Finish	2022		2023		2024		2025		2026		2027		2028		2029
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
46		Solaris Shalimar Tower - 8 (Phase 1B)	1621 days	Sat 11-02-23	Mon 01-01-29															
47		Piling	90 days	Sat 11-02-23	Tue 06-06-23															
48		Sub-Structure	100 days	Thu 13-06-24	Sat 02-11-24															
49		Superstructure	455 days	Wed 01-01-25	Mon 31-08-26															
50		Block Work	370 days	Tue 26-08-25	Fri 08-01-27															
51		Internal Plaster	400 days	Wed 15-10-25	Fri 02-04-27															
52		Internal Electrical	350 days	Fri 21-11-25	Mon 08-03-27															
53		Internal Plumbing	450 days	Fri 21-11-25	Wed 14-07-27															
54		Internal Finish	200 days	Wed 13-05-26	Tue 09-02-27															
55		Flooring	470 days	Tue 23-02-27	Fri 13-10-28															
56		Lift Installation	90 days	Tue 13-06-28	Mon 02-10-28															
57		External Plaster	120 days	Tue 12-01-27	Tue 22-06-27															
58		Aluminium Door Window	110 days	Thu 25-02-27	Fri 16-07-27															
59		Carpentry	300 days	Thu 19-08-27	Thu 07-09-28															
60		External Paint	90 days	Thu 03-06-27	Thu 23-09-27															
61		Ground Floor Finishes	150 days	Wed 03-03-27	Thu 09-09-27															
62		Electrical Infra	120 days	Sat 03-07-27	Tue 14-12-27															
63		Plumbing Infra	150 days	Fri 28-05-27	Tue 14-12-27															
64		Amenities	90 days	Mon 18-10-27	Tue 08-02-28															
65		De-Snagging & Handover	90 days	Tue 12-09-28	Mon 01-01-29															
66																				
67																				

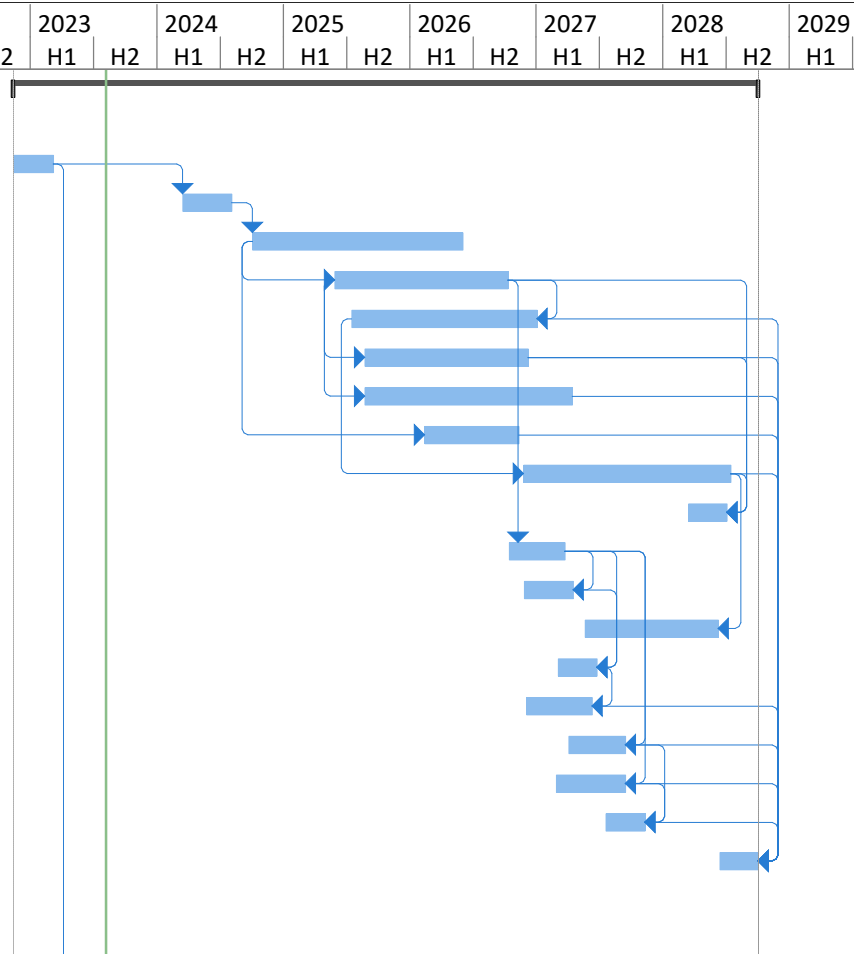

Project: msproj11
Date: Mon 06-11-23

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Progress	
Project Summary		Duration-only		Manual Progress	
External Tasks		Manual Summary Rollup			
External Milestone		Manual Summary			
