


ID	Task Mo	Task Name	Duration	Start	Finish	2018		2019		2020		2021		2022		2023		2024		2025		2026		2027		2028	
						H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
217		Tower - E,G,H,I,J,K (Phase 1)	1910 days	Fri 12-10-18	Wed 16-07-25																						
218		Land Development,Setting Out & Excavation	140 days	Fri 12-10-18	Tue 02-04-19																						
219		Piling	320 days	Thu 15-08-19	Thu 10-09-20																						
220		Sub-Structure	100 days	Fri 30-10-20	Tue 02-03-21																						
221		Superstructure	650 days	Fri 05-02-21	Wed 31-05-23																						
222		Block Work	450 days	Mon 14-03-22	Mon 13-11-23																						
223		Internal Plaster	360 days	Thu 01-09-22	Sat 13-01-24																						
224		Internal Electrical	780 days	Fri 17-06-22	Mon 19-05-25																						
225		Internal Plumbing	900 days	Mon 14-03-22	Wed 16-07-25																						
226		Internal Finish	300 days	Tue 14-09-21	Sat 15-10-22																						
227		Flooring	480 days	Mon 03-04-23	Fri 24-01-25																						
228		Lift Installation	180 days	Wed 13-12-23	Thu 08-08-24																						
229		External Plaster	300 days	Tue 15-11-22	Tue 26-12-23																						
230		Aluminium Door Window	360 days	Tue 03-01-23	Sat 11-05-24																						
231		Carpentry	360 days	Mon 13-11-23	Fri 21-03-25																						
232		External Paint	270 days	Tue 02-01-24	Mon 06-01-25																						
233		Ground Floor Finishes	200 days	Mon 08-04-24	Mon 06-01-25																						
234		Electrical Infra	270 days	Thu 17-08-23	Wed 21-08-24																						
235		Plumbing Infra	270 days	Thu 17-08-23	Wed 21-08-24																						
236		Driveway Incl. Parking	210 days	Mon 01-04-24	Sat 11-01-25																						
237		Amenities	180 days	Mon 22-04-24	Mon 23-12-24																						
238		De-Snagging & Handover	180 days	Tue 09-07-24	Sat 15-03-25																						

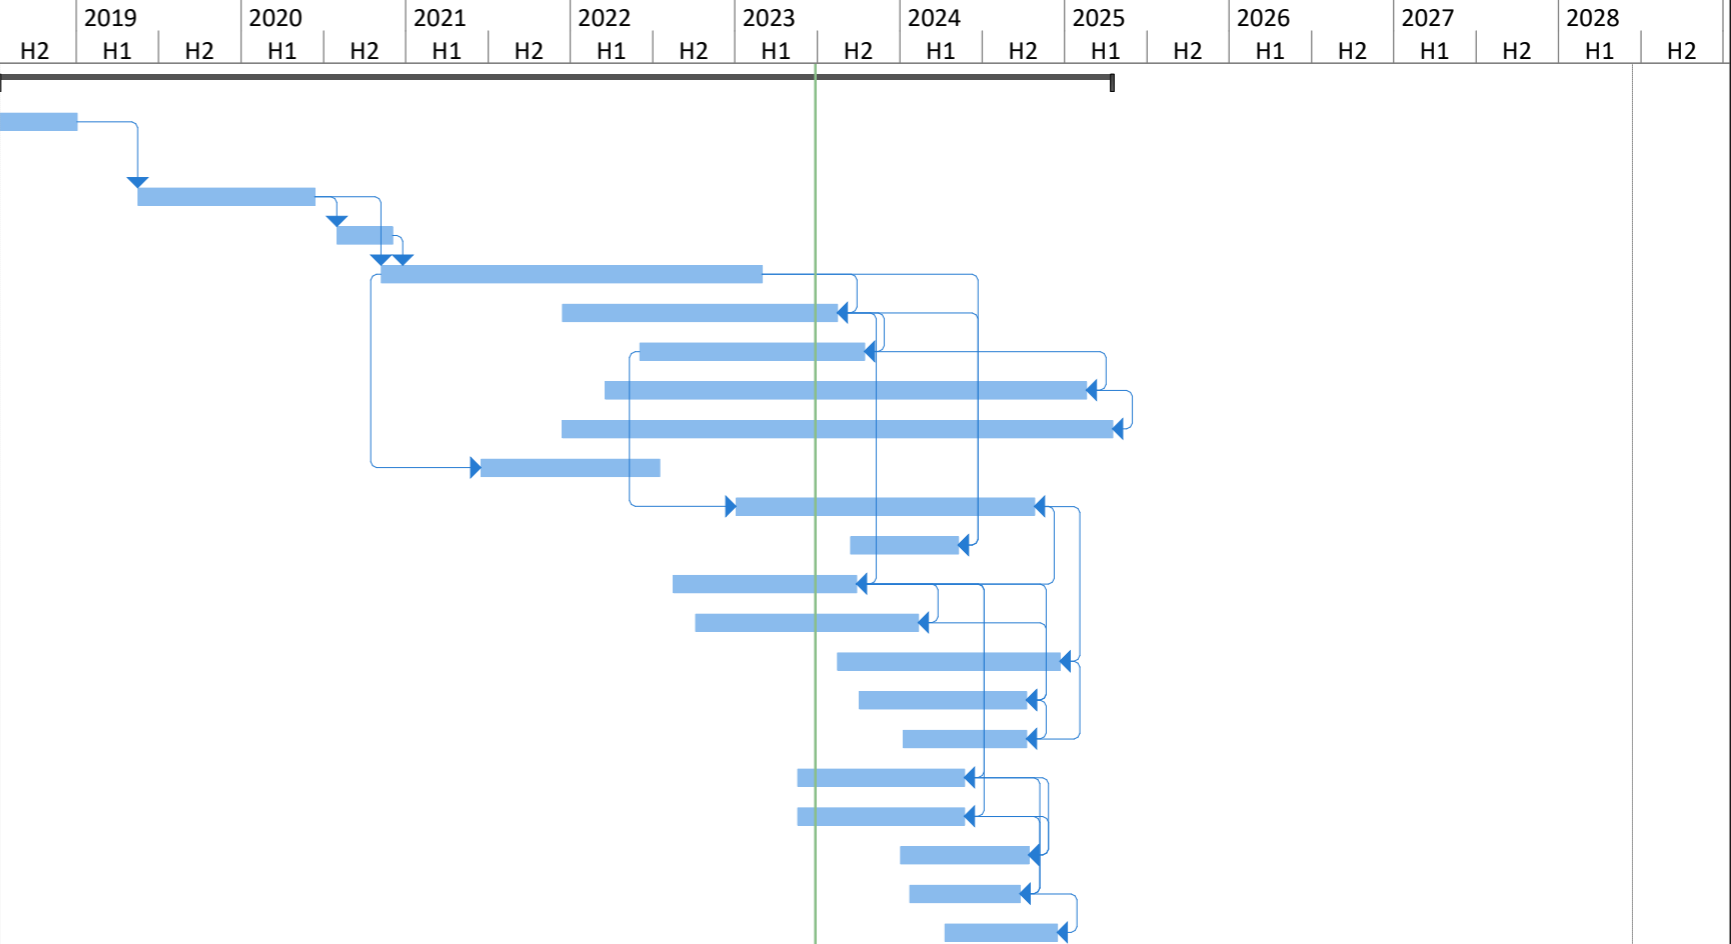

Project: msproj11 Date: Wed 27-09-23	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			
