


ID	Task Name	Duration	Start	Finish
1	Master Construction Programe-Solaris Joka Ph-2	1306 days	Fri 29-07-22	Thu 10-06-27
2	Piling	156 days	Fri 29-07-22	Tue 07-03-23
3	Sub-Structure	159 days	Thu 09-09-23	Thu 28-09-23
4	Superstructure	436 days	Thu 22-06-23	Tue 18-02-25
5	Block Work	434 days	Wed 13-12-23	Tue 22-07-25
6	Internal Plaster	392 days	Thu 21-03-24	Fri 29-08-25
7	Internal Electrical	776 days	Thu 01-02-24	Fri 11-12-26
8	Internal Plumbing	832 days	Wed 07-02-24	Thu 04-09-27
9	Internal Finish	599 days	Fri 01-11-24	Tue 12-01-27
10	Flooring	536 days	Fri 20-12-24	Fri 11-12-26
11	Lift Installation	365 days	Mon 16-12-24	Tue 21-04-26
12	External Plaster	254 days	Mon 16-09-24	Fri 29-08-25
13	Aluminium Door Window	320 days	Fri 15-11-24	Mon 19-01-26
14	Carpentry	451 days	Fri 08-08-25	Tue 13-04-27
15	External Paint	340 days	Thu 10-07-25	Tue 06-10-26
16	Ground Floor Finishes	131 days	Mon 20-04-26	Tue 06-10-26
17	Electrical Infra	112 days	Wed 25-02-26	Tue 21-07-26
18	Plumbing Infra	163 days	Mon 29-12-25	Sat 01-08-26
19	Driveway Incl. Parking	148 days	Thu 07-05-26	Mon 28-11-26
20	Amenities	112 days	Wed 24-06-26	Mon 28-11-26
21	De-Shagging & Handover	223 days	Tue 11-08-26	Thu 10-06-27

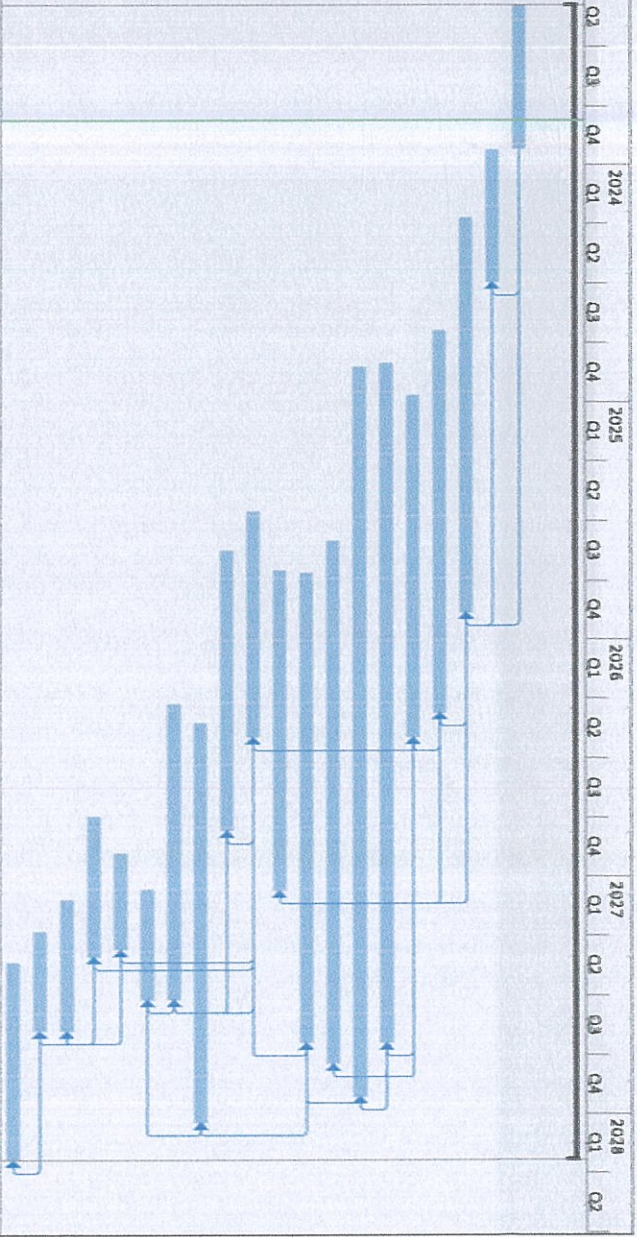

EDEN REALTY VENTURES PVT. LTD.

[Signature]
Director

Project: mspjpr011
Date: Mon 28-01-23

Task Summary: **Task** (Blue bar), **External Task** (Dotted bar), **External Milestone** (Diamond), **Inactive Task** (Grey bar), **Inactive Milestone** (Diamond), **Manual Task** (Light Blue bar), **Manual Summary** (Light Blue bar), **Manual Summary Rollup** (Light Blue bar), **Deadline** (Light Blue bar), **Progress** (Light Blue bar), **Manual Progress** (Light Blue bar)

Milestone Summary: **Split** (Blue bar), **Milestone** (Blue bar)

Page 1
