






Department	Information Required	Status	
	Status of Project:		
	Status of Construction of Each Building with Photographs	All Sub Structure Work Completed Superstructure And Finishing Work In Progress	
	Building Name -	BLOCK-11-PHASE V	Remarks
	Main Entrance		
	Building Elevation		
	Gr. Floor Surrounding Area		
	Gr. Floor Lobby Entrance		
Projects	Super Structure		Roof
	MS Balcony		Completed
	Inside Apartment		Completed
	Kitchen Counter		Completed
	Toilet		Completed
	Staircase		Completed

Department	Information Required	Status	
Projects	Status of Projects Status of Construction of Each Building with Photographs	All Sub Structure Work Completed Superstructure And Finishing Work In Progress	
	Building Name -	BLOCK-12-PHASE V	Remarks
	Main Entrance		
	Building Elevation		
	Kids Play Area		
	Gr. Floor Lobby Entrance		
	Super Structure		Completed
	MS Balcony		Completed
	INSIDE APARTMENT		Completed
	Kitchen Counter		Completed
Toilet		Completed	
Staircase		Completed	

Department	Information Required
	Status of Project:
	Status of Construction of Each Building with Photographs
	Building Name -
	Main Entrance

Building Elevation

Projects

Super Structure

Brickwork

Tiles Work

Balcony Railing

MS Stair Railing

Status

BLOCK-13-PHASE VI









Remarks / Any Issues

15th Floor Slab Casting Completed

**1st Floor Flat 60% And 2nd To 10th Floor Flat BW
Completed,11th Floor BW 85% Completed**

Started From 2nd Floor


2nd Floor To 7th & 9th Floor Completed

Started From 2nd Floor

Department	Information Required
	Status of Project:
	Status of Construction of Each Building with Photographs
	Building Name -
	Main Entrance



Projects

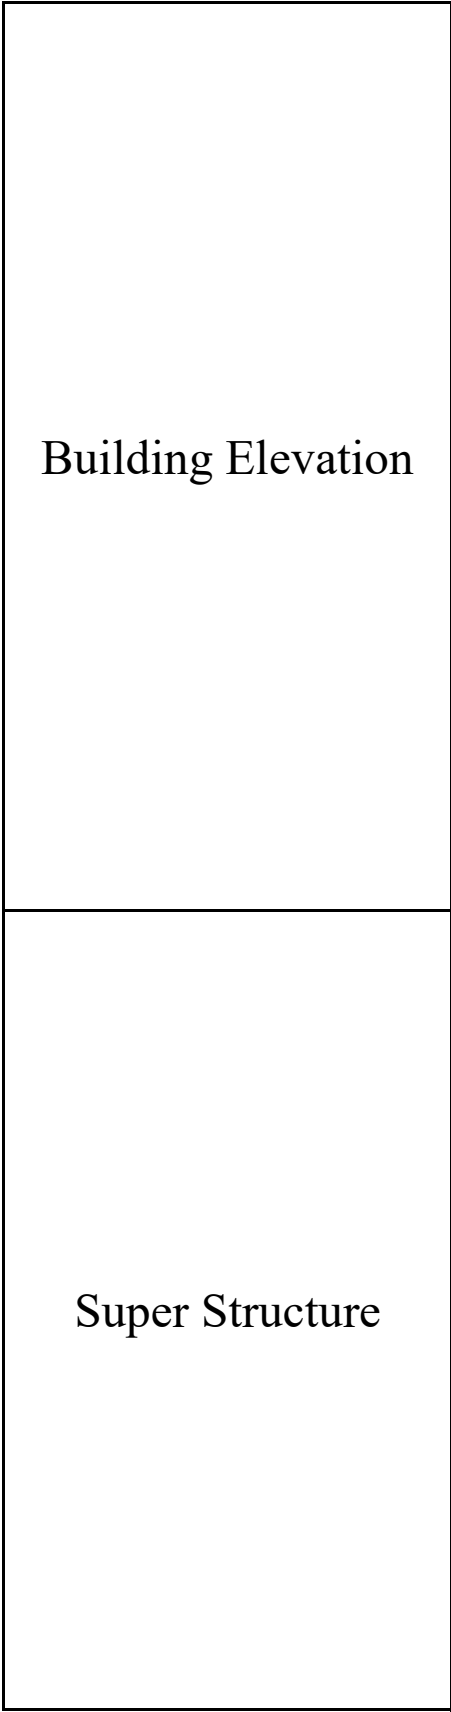

Building Elevation


Super Structure

Brickwork

Gypsum Putty

Tiles Work

Balcony Railing

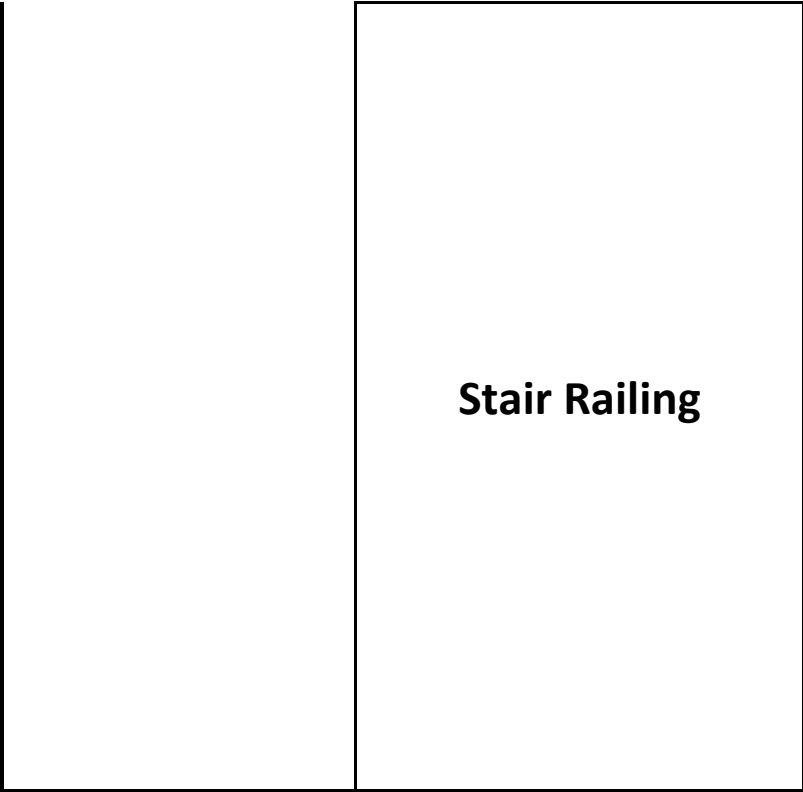

Stair Railing

Sta

All Sub Structure Work Completed Super

BLOCK-14,PART-1-PHASE VI











tus

structure And Finishing Work In Progress

BLOCK-14,PART-2-PHASE VI











Remarks / Any Issues	
Part-1	Part-2

15th Floor Slab Completed	14th Floor Slab Completed

**11th Floor Completed,12th
Floor 75% Done**

**10th Floor Completed,11th
Floor 70% Done**

**1st To 5th Floor Completed,
6th Floor WIP**

**1st To 2nd Floor
Completed, 3rd To 4th
Floor WIP**

**1st To 6th Floor Completed
Except F & A Flat(Master
Bed Room & Bed Room) &
Balcony, 7th Floor WIP**

**1st To 6th Floor Completed
Except G & K Flat(Master
Bed Room & L/D Partially)
& Balcony, 7th Floor WIP**

**1st To 8th Floor Completed,
9th & 10th Floor WIP**

**1st To 8th Floor Completed,
7th To 11th Floor WIP**

**1st To 4th Floor
Completed,5th & 6th WIP**

**1st To 4th Floor
Completed,5th & 6th WIP**

Department	Information Required
	Status of Project:
	Status of Construction of Each Building with Photographs
	Building Name -
	Main Entrance




Building Elevation



Super Structure

Projects

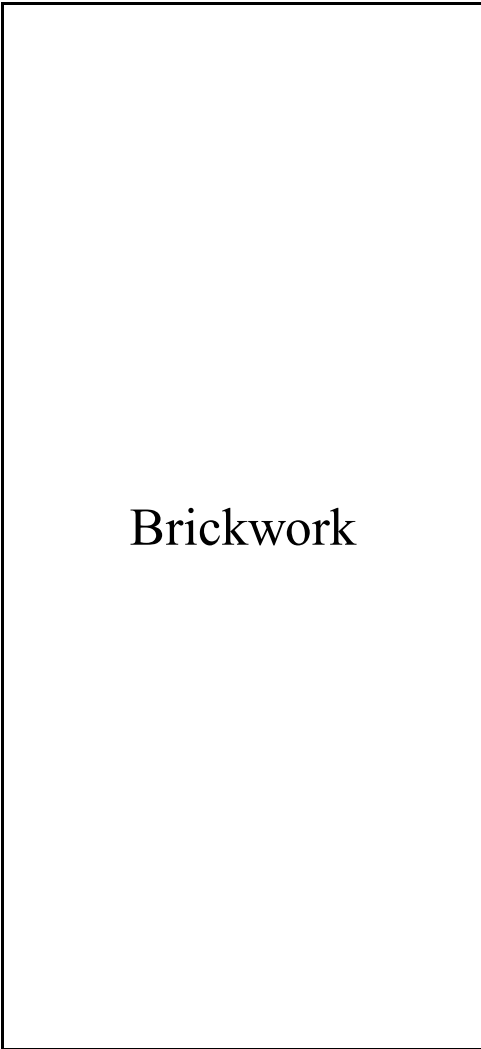

Brickwork

Tiles Work

Balcony Railing

Stair Railing

Status

BLOCK-15, PHASE VI














Remarks / Any Issues



13th Floor Slab Casting Completed

1st To 7th Floor Completed

1st Floor Completed

1st Floor Completed

1st Floor Completed

Department	Information Required
	Status of Project:
	Status of Construction of Each Building with Photographs
	Building Name -
	Main Entrance

Building Elevation

Projects

Super Structure

MS Work

Brickwork

Gypsum Putty

Tiles Work

MS Stair Railing

Status

BLOCK-16,PHASE VI











Remarks / Any Issues

16th Floor Slab Complete

1st To 10th Floor Complete Except C Flat

1st To 12th Floor Complete

1st To 4th Floor Complete,5th To 7th WIP

1st To 9th Floor Complete Without Balcony

1st To 10th Floor Complete

Department	Information Required
	Status of Project:
	Status of Construction of Each Building with Photographs
	Building Name -
	Main Entrance

Projects

**Building Elevation
&
Superstructure**

Status

All Sub Structure Work Completed Superstructure And Finishing Work In Progress

BLOCK-MLCP,PHASE VI





Remarks / Any Issues

Roof And Above Roof Slab Completed

