


ID	Task Mode	Task Name	Duration	Start	Finish	November 21		January 11		March 1		April 21		June 11		August 1		September 21		Nov
						9/6	3/27	10/16	5/7	11/26	6/17	1/6	7/28	2/16	9/6	3/28	10/17	5/8	11/27	
0		SIDDHA SKY PROJECT G+31 3 NOS BUILDING , 2207 B+G+7 MLCP , SKYWALK & CLUB	2207 days	Thu 11/24/16	Fri 12/30/22															
1		SIDDHA SKY	2207 days	Thu 11/24/16	Fri 12/30/22															
2		BLOCK-1 G + 31	1937 days	Fri 5/12/17	Mon 9/19/22															
3	✓	PILING	273 days	Fri 5/12/17	Thu 2/8/18															
4	✓	SUBSTRUCTURE	172 days	Fri 2/9/18	Mon 7/30/18															
5	✓	GROUND FLOOR ROOF	47 days	Tue 7/31/18	Sat 9/15/18															
6		1ST FLOOR ROOF TO 31ST FLOOR ROOF	886 days	Sun 9/16/18	Sun 2/28/21															
7		FINISHING	800 days	Mon 12/23/19	Tue 3/15/22															
8		SERVICES	400 days	Wed 2/3/21	Tue 3/15/22															
9		GROUND FLOOR LOBBY & PARKING	270 days	Wed 7/14/21	Thu 4/14/22															
10		SNAGGING & DESNAGGING	160 days	Fri 1/14/22	Fri 6/24/22															
11		FLAT HANDOVER	100 days	Fri 6/10/22	Mon 9/19/22															
12		BLOCK-2 G + 31	1983 days	Tue 1/10/17	Sun 7/3/22															
13	✓	PILING	411 days	Tue 1/10/17	Sat 2/24/18															
14	✓	SUBSTRUCTURE	109 days	Sun 2/25/18	Wed 6/13/18															
15	✓	GROUND FLOOR ROOF	95 days	Thu 6/14/18	Sun 9/16/18															
16		1ST FLOOR ROOF TO 31ST FLOOR ROOF	678 days	Mon 9/17/18	Fri 7/31/20															
17		FINISHING	850 days	Fri 5/31/19	Mon 10/11/21															
18		SERVICES	420 days	Mon 11/2/20	Sun 1/2/22															
19		GROUND FLOOR AND LOBBY PARKING	270 days	Mon 6/1/20	Tue 3/2/21															
20		SNAGGING & DESNAGGING	190 days	Tue 8/10/21	Sun 2/20/22															
21		FLAT HANDOVER	130 days	Wed 2/23/22	Sun 7/3/22															
22		BLOCK-3 G+31	2013 days	Thu 11/24/16	Thu 6/16/22															
23	✓	PILING	208 days	Thu 11/24/16	Mon 6/19/17															
24	✓	SUBSTRUCTURE	88 days	Tue 6/20/17	Fri 9/15/17															
25	✓	GROUND FLOOR ROOF	38 days	Sat 9/16/17	Mon 10/23/17															
26	✓	1ST FLOOR ROOF TO 31ST FLOOR ROOF	677 days	Tue 10/24/17	Sun 9/1/19															
27		FINISHING	950 days	Mon 2/4/19	Fri 9/24/21															
28		SERVICES	450 days	Mon 9/7/20	Wed 12/8/21															
29		GROUND FLOOR LOBBY & PARKING	300 days	Mon 3/1/21	Wed 12/29/21															
30		SNAGGING & DESNAGGING	190 days	Sun 7/25/21	Fri 2/4/22															
31		FLAT HANDOVER	130 days	Sun 2/6/22	Thu 6/16/22															
32		COMMON DEVELOPEMENT	858 days	Mon 8/10/20	Fri 12/30/22															
33		SKY WALK	858 days	Mon 8/10/20	Fri 12/30/22															
34		MLCP	700 days	Mon 1/4/21	Thu 12/15/22															
35		CLUB	630 days	Mon 3/1/21	Wed 11/30/22															
36		INFRASTRUCTURE	530 days	Mon 5/3/21	Sun 10/23/22															
37		PODIUM	450 days	Mon 9/6/21	Wed 12/7/22															

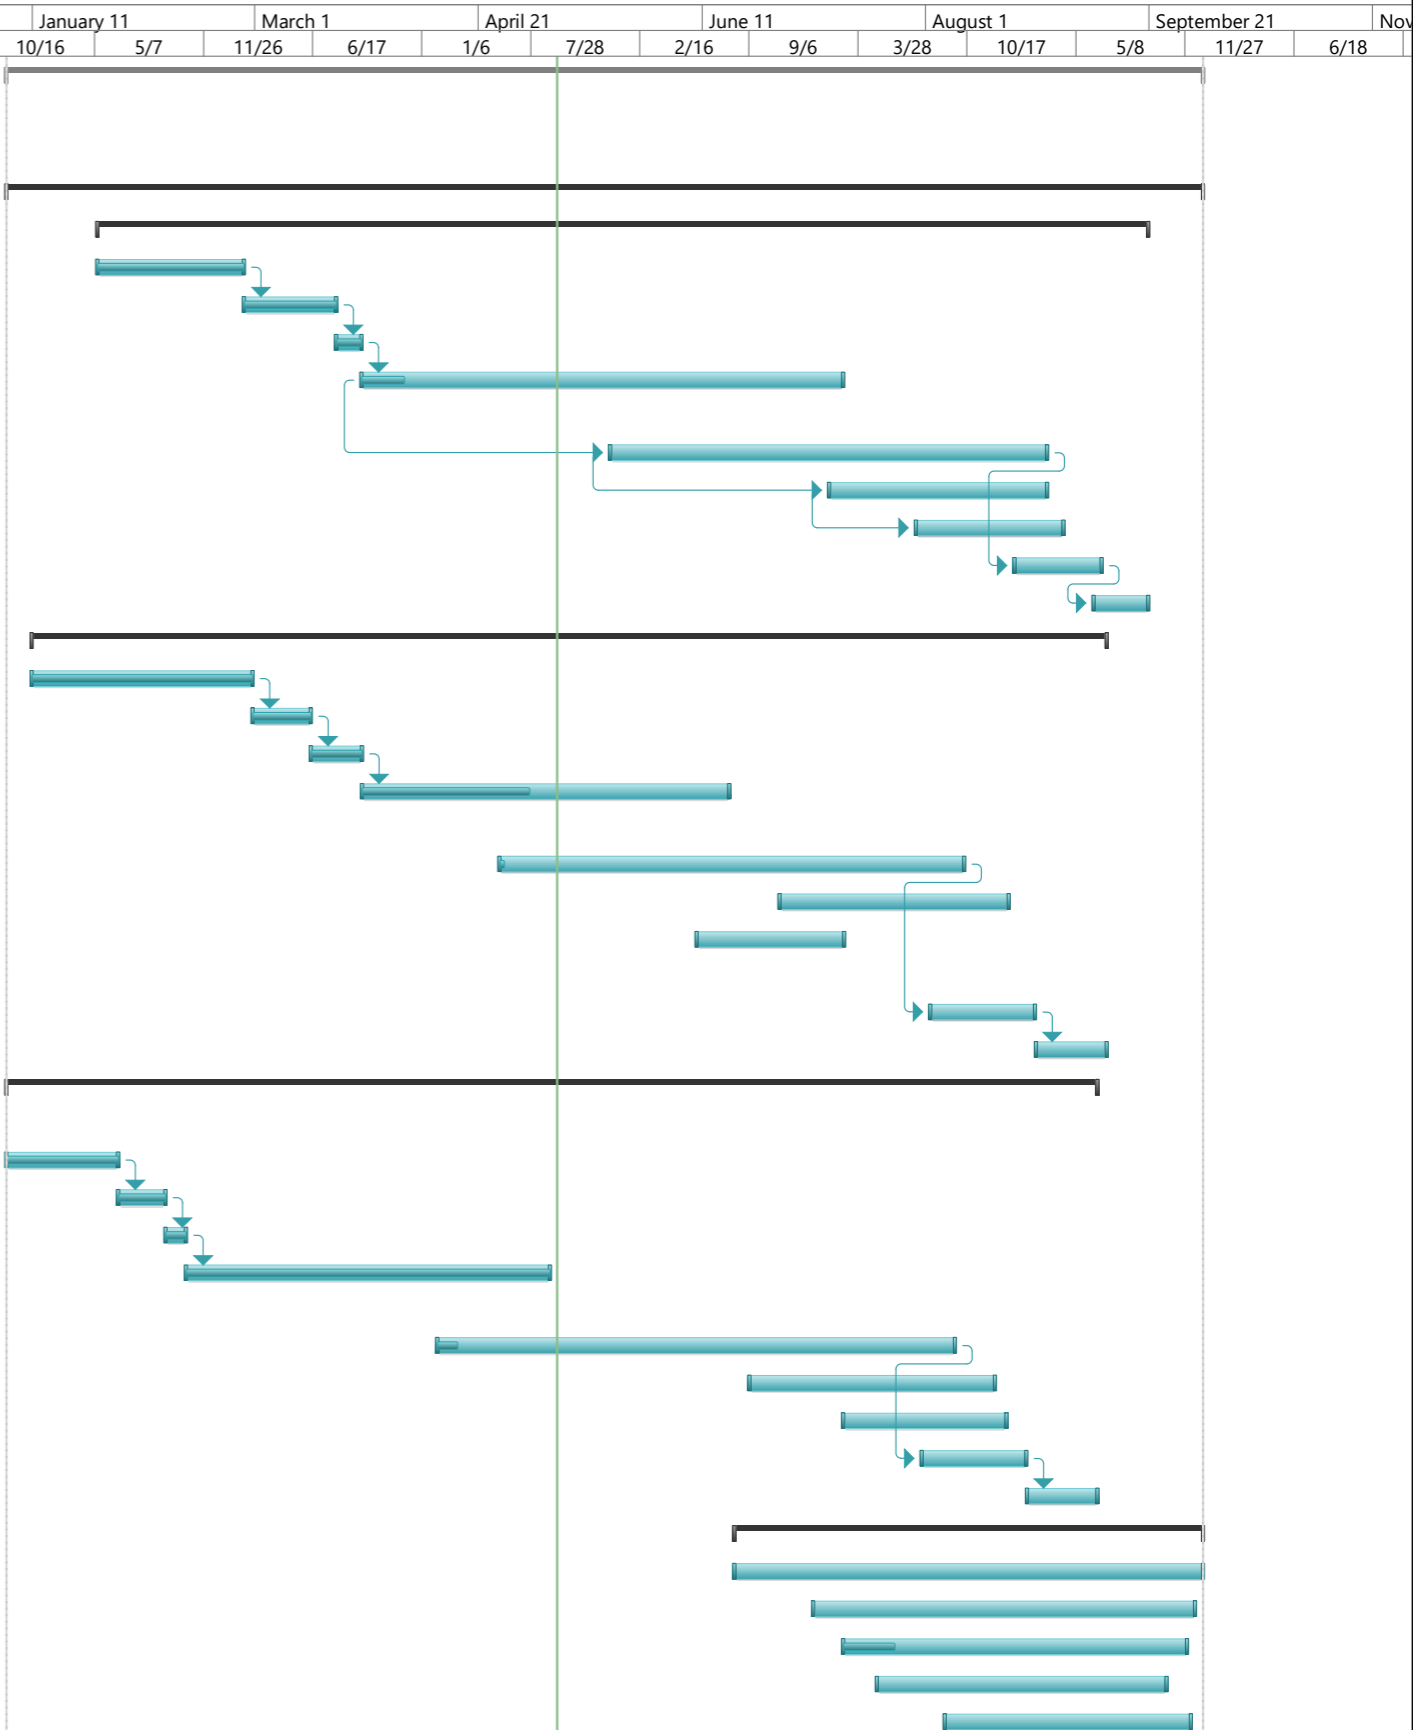

Project: SIDDHA SKY PROJECT G
Date: Sun 9/15/19

Task		Project Summary		Manual Task		Start-only		Finish-only		External Tasks		Manual Progress		External Milestone
Split		Inactive Task		Duration-only		External Milestone		Manual Progress		External Milestone		Manual Progress		External Milestone
Milestone		Inactive Milestone		Manual Summary Rollup		External Milestone		Manual Progress		External Milestone		Manual Progress		External Milestone
Summary		Inactive Summary		Manual Summary		External Milestone		Manual Progress		External Milestone		Manual Progress		External Milestone
