ENGINEER'S CERTIFICATE

Date: 19.09.2019

Subject: Certificate of Progress of Work for Development of Hiland Green Phase 1A, for Construction

of 14 nos. of building(s) of Calcutta Riverside, 1 New Bata Road, Batanagar, ward no 27 & 28,

Maheshtala, Kolkata 700140.

Ref: HIRA Registration NPR Number 00734

I, Asish Misra, being Project Engineer of M/s RIVERBANK DEVELOPERS PRIVATE LIMITED, hereby,

certifying the Progress of work done for the project Hiland Greens Phase 1A, of Calcutta Riverside, 1

New Bata Road, Batanagar, ward no 27 & 28, Maheshtala, Kolkata 700140, admeasuring built up area

123979.30 sq. mts. which is proposed to be registered under WBHIRA.

1. I have estimated the percentage of completion of work to obtain Occupation Certificate/

Completion Certificate, of the Civil, MEP and Allied works, of the Building(s) of the project

mentioned above. As per my estimate, work progress is based on the actual status at site.

2. I certify that the Work progress of the Civil, MEP and allied work for the aforesaid Project as

completed on the date of this certificate is as given in Table A below:

Project Engineer

Riverbank Developers Private Limited



TABLE A

ITEM			% A(pletion up to JUNE-2019 "Hiland Greens Phase – 1A"										
	T13	T14	T15	T16	T17	T18	T19	T20	T21	T22	T23	T24	T25	T26
Pile	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%
Pile Cap	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%
Tiebeam	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%
RCC Structure	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%
Flooring Work	95%	95%	90%	90%	86%	98%	98%	95%	92%	85%	98%	95%	94%	78%
Aluminium Window Fixing	84%	84%	0%	0%	0%	84%	93%	64%	67%	18%	77%	82%	74%	0%
Balcony Railing Fixing	93%	93%	93%	55%	40%	97%	97%	97%	100%	40%	93%	93%	93%	43%
Stair Railing Fixing	100%	100%	100%	40%	0%	100%	100%	100%	100%	0%	100%	100%	100%	87%
False Ceiling Work	80%	80%	0%	0%	0%	90%	90%	90%	75%	18%	80%	80%	0%	0%
Wall Putty Up to Sil	100%	93%	92%	81%	75%	98%	95%	100%	93%	59%	85%	87%	87%	57%
Wall Putty Below Sil	100%	93%	55%	42%	20%	90%	90%	74%	80%	0%	31%	73%	0%	0%
Balcony Railing Paint	25%	25%	0%	0%	0%	0%	61%	60%	0%	0%	25%	25%	0%	0%
Stair Railing Paint	0%	0%	0%	0%	0%	0%	61%	60%	0%	0%	0%	0%	0%	0%
Door Frame Fixing	90%	95%	72%	73%	73%	100%	100%	85%	75%	66%	95%	95%	52%	29%
Flush Door Shutter Fixing	38%	65%	17%	17%	0%	90%	95%	15%	35%	13%	55%	75%	8%	0%
External Painting Work	90%	80%	75%	75%	30%	85%	75%	83%	75%	85%	95%	90%	50%	50%
Flush Door Shutter Painting	0%	0%	0%	0%	0%	50%	35%	0%	0%	0%	0%	0%	0%	0%
Door Hardware Fixing	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%
Duct Cover Fixing											1			
Internal Electrical Work														
Slab & Wall Conduiting & Modular Box Fixing	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%	100%
Wiring & Switch/Socket Fixing	5%	5%	5%	5%	5%	5%	5%	5%	5%	5%	5%	5%	5%	5%
Cover Plate Fixing	5%	5%	5%	5%	5%	5%	5%	5%	5%	0%	5%	5%	5%	5%
Internal PHE Work	96%	100%	100%	96%	96%	100%	96%	96%	96%	96%	100%	100%	96%	96%
Water proof Testing with screed	96%	96%	96%	96%	96%	96%	96%	96%	96%	96%	96%	96%	96%	96%
CP Fittings & Sanitary Ware Fixing	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%
External Electrical Work	90%													
External PHE Work	96%													
Landscape (Hard scape & Soft scape)							8	0%						
Intra Land parcel Roads							9	1%						
Elevators	90%	90%	75%	75%	75%	80%	75%	75%	75%	75%	90%	90%	90%	75%

Project Engineer

Twi Sw.

Riverbank Developers Private Limited

Riverbank Developers Pvt. Ltd. **Registered Office**

225C, AJC Bose Road, 4th Floor, Kolkata - 700020, India P: +91 33 2283 9015-17 F: +91 33 2289 2148 W: www.hiland.in **Sales and Marketing Office**

Calcutta Riverside, 1, New Bata Road, Mahestala Municipality,

Kolkata 700 140

P: 033 2490-5491/ 6970 E: sales@hilandcal.com

CIN: U70101WB2007PTC120037

I Parism.














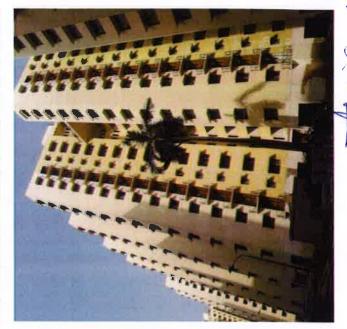










Aurism!





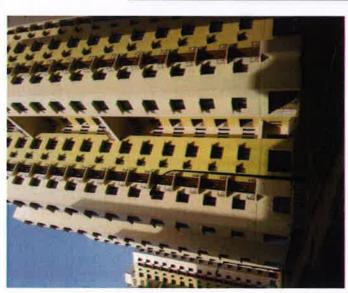

Mismi
