


# Project : SOLARIS MALL, SERAMPORE.

EDEN INFRABUILD PVT. LTD.

ID	Task Mode	Task Name	Duration	Start	Finish	2019	2020	2021	2022	2023	2024
						H1	H2	H1	H2	H1	H2
1		<b>Project : Solaris Mall, Serampore.</b>	<b>1196 days</b>	<b>Sat 15 Dec '18</b>	<b>Wed 16 Nov '22</b>						
2		Mobilization of Piling contractor	15 days	Sat 15 Dec '18	Tue 01 Jan '19						
3		Site Cleaning & Dressing	25 days	Tue 01 Jan '19	Tue 29 Jan '19						
4		Construction of Site office & Labour Hutment	35 days	Wed 23 Jan '19	Fri 01 Mar '19						
5		Pilling Work	100 days	Tue 19 Feb '19	Sat 15 Jun '19						
6		Civil & Structure work	547 days	Thu 30 May '19	Fri 19 Mar '21						
7		Internal & External Finishing work	540 days	Mon 21 Oct '19	Thu 08 Jul '21						
8		Door, window & Glazing work	475 days	Wed 12 Feb '20	Thu 26 Aug '21						
9		MEP internal & external	535 days	Fri 22 May '20	Mon 14 Feb '22						
10		Multiplex Finishing work	300 days	Tue 23 Mar '21	Fri 11 Mar '22						
11		Landscaping & Hardscaping work	180 days	Thu 23 Sep '21	Thu 21 Apr '22						
12		Solar Pannel Installation	180 days	Fri 15 Oct '21	Thu 19 May '22						
13		Technical Inspection	90 days	Thu 21 Apr '22	Tue 02 Aug '22						
14		Rectification (If required)	100 days	Fri 24 Jun '22	Fri 28 Oct '22						
15		Handover	25 days	Wed 28 Sep '22	Wed 16 Nov '22						

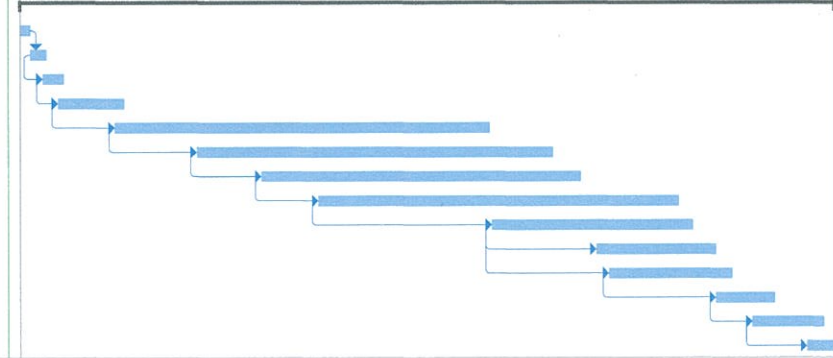

EDEN INFRABUILD PVT. LTD.

*Kumar Satyab.*

Director

Project:  
Date: Sat 24 Nov '18

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
