BLOCK-9

ID	Task Name	Duration	Start	Finish	Predecessors
1	**Elita Garden Vista Project**	**714 days**	**Mon 05-02-18**	**Sun 19-01-20**	
2					
3	**Block-09**	**714 days**	**Mon 05-02-18**	**Sun 19-01-20**	
4	**Electrical work Internal**	**270 days**	**Mon 05-02-18**	**Thu 01-11-18**	
5	Gr. Floor to 13th Floor	50 days	Mon 05-02-18	Mon 26-03-18	
6	14th to 18th Floor	15 days	Thu 18-10-18	Thu 01-11-18	5SS+255 days
7	**Plumbing work Internal**	**265 days**	**Mon 05-02-18**	**Sat 27-10-18**	
8	Gr. Floor to 13th Floor	60 days	Mon 05-02-18	Thu 05-04-18	5SS
9	14th to 18th Floor	10 days	Thu 18-10-18	Sat 27-10-18	6SS
10	**Fire fighting work**	**270 days**	**Mon 19-02-18**	**Thu 15-11-18**	
11	Gr. Floor to 13th Floor	55 days	Mon 19-02-18	Sat 14-04-18	8SS+14 days
12	14th to 18th Floor	15 days	Thu 01-11-18	Thu 15-11-18	9SS+14 days
13	**M. S. Railing work**	**273 days**	**Thu 08-03-18**	**Wed 05-12-18**	
14	Gr. Floor to 13th Floor	100 days	Thu 08-03-18	Fri 15-06-18	11SS+17 days
15	14th to 18th Floor	18 days	Sun 18-11-18	Wed 05-12-18	12SS+17 days
16	**HVAC pipe & drain work**	**263 days**	**Sat 07-07-18**	**Tue 26-03-19**	
17	Gr. Floor to 13th Floor	35 days	Sat 07-07-18	Fri 10-08-18	14SS+121 days
18	14th to 18th Floor	8 days	Tue 19-03-19	Tue 26-03-19	15SS+121 days
19	**Putty Wall finish (Part work)**	**269 days**	**Sat 08-09-18**	**Mon 03-06-19**	
20	Gr. Floor to 13th Floor	55 days	Sat 08-09-18	Thu 01-11-18	17SS+63 days
21	14th to 18th Floor	14 days	Tue 21-05-19	Mon 03-06-19	18SS+63 days
22	**Tile laying work (with Granite fixing)**	**285 days**	**Mon 08-10-18**	**Fri 19-07-19**	
23	Gr. Floor to 13th Floor	110 days	Mon 08-10-18	Fri 25-01-19	20SS+30 days
24	14th to 18th Floor	30 days	Thu 20-06-19	Fri 19-07-19	21SS+30 days
25	**False ceiling work (Only G.I. Structure work)**	**269 days**	**Mon 08-10-18**	**Wed 03-07-19**	
26	Gr. Floor to 13th Floor	35 days	Mon 08-10-18	Sun 11-11-18	23SS
27	14th to 18th Floor	14 days	Thu 20-06-19	Wed 03-07-19	24SS
28	**Alluminium window work**	**265 days**	**Mon 22-10-18**	**Sat 13-07-19**	
29	Gr. Floor to 13th Floor	50 days	Mon 22-10-18	Mon 10-12-18	26SS+14 days
30	14th to 18th Floor	10 days	Thu 04-07-19	Sat 13-07-19	27SS+14 days
31	**Divertor fixing**	**270 days**	**Mon 22-10-18**	**Thu 18-07-19**	
32	Gr. Floor to 13th Floor	75 days	Mon 22-10-18	Fri 04-01-19	29SS
33	14th to 18th Floor	15 days	Thu 04-07-19	Thu 18-07-19	30SS
34	**Lift**	**275 days**	**Thu 01-11-18**	**Fri 02-08-19**	
35	Gr. Floor to 13th Floor	70 days	Thu 01-11-18	Wed 09-01-19	32SS+10 days
36	14th to 18th Floor	20 days	Sun 14-07-19	Fri 02-08-19	33SS+10 days
37	**A.C ledge grill fixing**	**264 days**	**Wed 21-11-18**	**Sun 11-08-19**	
38	Gr. Floor to 13th Floor	30 days	Wed 21-11-18	Thu 20-12-18	32SS+30 days
39	14th to 18th Floor	9 days	Sat 03-08-19	Sun 11-08-19	33SS+30 days
40	**Wire pulling & Switch fixing**	**267 days**	**Sat 22-12-18**	**Sat 14-09-19**	
41	Gr. Floor to 13th Floor	60 days	Sat 22-12-18	Tue 19-02-19	38SS+31 days
42	14th to 18th Floor	12 days	Tue 03-09-19	Sat 14-09-19	39SS+31 days
43	**HVAC copper pipe fixing**	**270 days**	**Sat 22-12-18**	**Tue 17-09-19**	
44	Gr. Floor to 13th Floor	80 days	Sat 22-12-18	Mon 11-03-19	41SS
45	14th to 18th Floor	15 days	Tue 03-09-19	Tue 17-09-19	42SS
46	**Putty finish work**	**267 days**	**Sun 06-01-19**	**Sun 29-09-19**	
47	Gr. Floor to 13th Floor	75 days	Sun 06-01-19	Thu 21-03-19	44SS+15 days
48	14th to 18th Floor	12 days	Wed 18-09-19	Sun 29-09-19	45SS+15 days
49	**False ceiling finish work**	**267 days**	**Wed 09-01-19**	**Wed 02-10-19**	
50	Gr. Floor to 13th Floor	90 days	Wed 09-01-19	Mon 08-04-19	47FS+3 days
51	14th to 18th Floor	12 days	Sat 21-09-19	Wed 02-10-19	48SS+3 days
52	**HVAC outdoor unit fixing**	**264 days**	**Tue 05-02-19**	**Sat 26-10-19**	
53	Gr. Floor to 13th Floor	35 days	Tue 05-02-19	Mon 11-03-19	44SS+45 days
54	14th to 18th Floor	9 days	Fri 18-10-19	Sat 26-10-19	45SS+45 days
55	**Door frame & shutter fixing incl: iron mongeries**	**265 days**	**Wed 20-02-19**	**Mon 11-11-19**	
56	Gr. Floor to 13th Floor	60 days	Wed 20-02-19	Sat 20-04-19	50SS+42 days
57	14th to 18th Floor	10 days	Sat 02-11-19	Mon 11-11-19	51SS+42 days
58	**Sprinkler & Detector fixing work**	**265 days**	**Wed 20-02-19**	**Mon 11-11-19**	
59	Gr. Floor to 13th Floor	60 days	Wed 20-02-19	Sat 20-04-19	56SS
60	14th to 18th Floor	10 days	Sat 02-11-19	Mon 11-11-19	57SS
61	**HVAC indoor finish**	**265 days**	**Fri 08-03-19**	**Wed 27-11-19**	
62	Gr. Floor to 13th Floor	50 days	Fri 08-03-19	Fri 26-04-19	53SS+31 days
63	14th to 18th Floor	10 days	Mon 18-11-19	Wed 27-11-19	54SS+31 days
64	**Tile grout work**	**223 days**	**Sun 28-04-19**	**Fri 06-12-19**	
65	Gr. Floor to 13th Floor	30 days	Sun 28-04-19	Mon 27-05-19	62FS+1 day
66	14th to 18th Floor	8 days	Fri 29-11-19	Fri 06-12-19	63FS+1 day
67	**Primer over Internal Putty work**	**225 days**	**Sat 18-05-19**	**Sat 28-12-19**	
68	Gr. Floor to 13th Floor	45 days	Sat 18-05-19	Mon 01-07-19	65SS+20 days
69	14th to 18th Floor	8 days	Thu 19-12-19	Thu 26-12-19	66SS+20 days
70	**Sanitary ware & C.P fittings fixing**	**225 days**	**Sat 18-05-19**	**Sat 28-12-19**	
71	Gr. Floor to 13th Floor	40 days	Sat 18-05-19	Wed 26-06-19	68SS
72	14th to 18th Floor	10 days	Thu 19-12-19	Sat 28-12-19	69SS
73	**Shower curtain work**	**227 days**	**Sat 18-05-19**	**Mon 30-12-19**	
74	Gr. Floor to 13th Floor	44 days	Sat 18-05-19	Sun 30-06-19	68SS
75	14th to 18th Floor	12 days	Thu 19-12-19	Mon 30-12-19	69SS
76	**Handing Over**	**203 days**	**Mon 01-07-19**	**Sun 19-01-20**	
77	Gr. Floor to 13th Floor	60 days	Mon 01-07-19	Thu 29-08-19	74
78	14th to 18th Floor	20 days	Tue 31-12-19	Sun 19-01-20	75

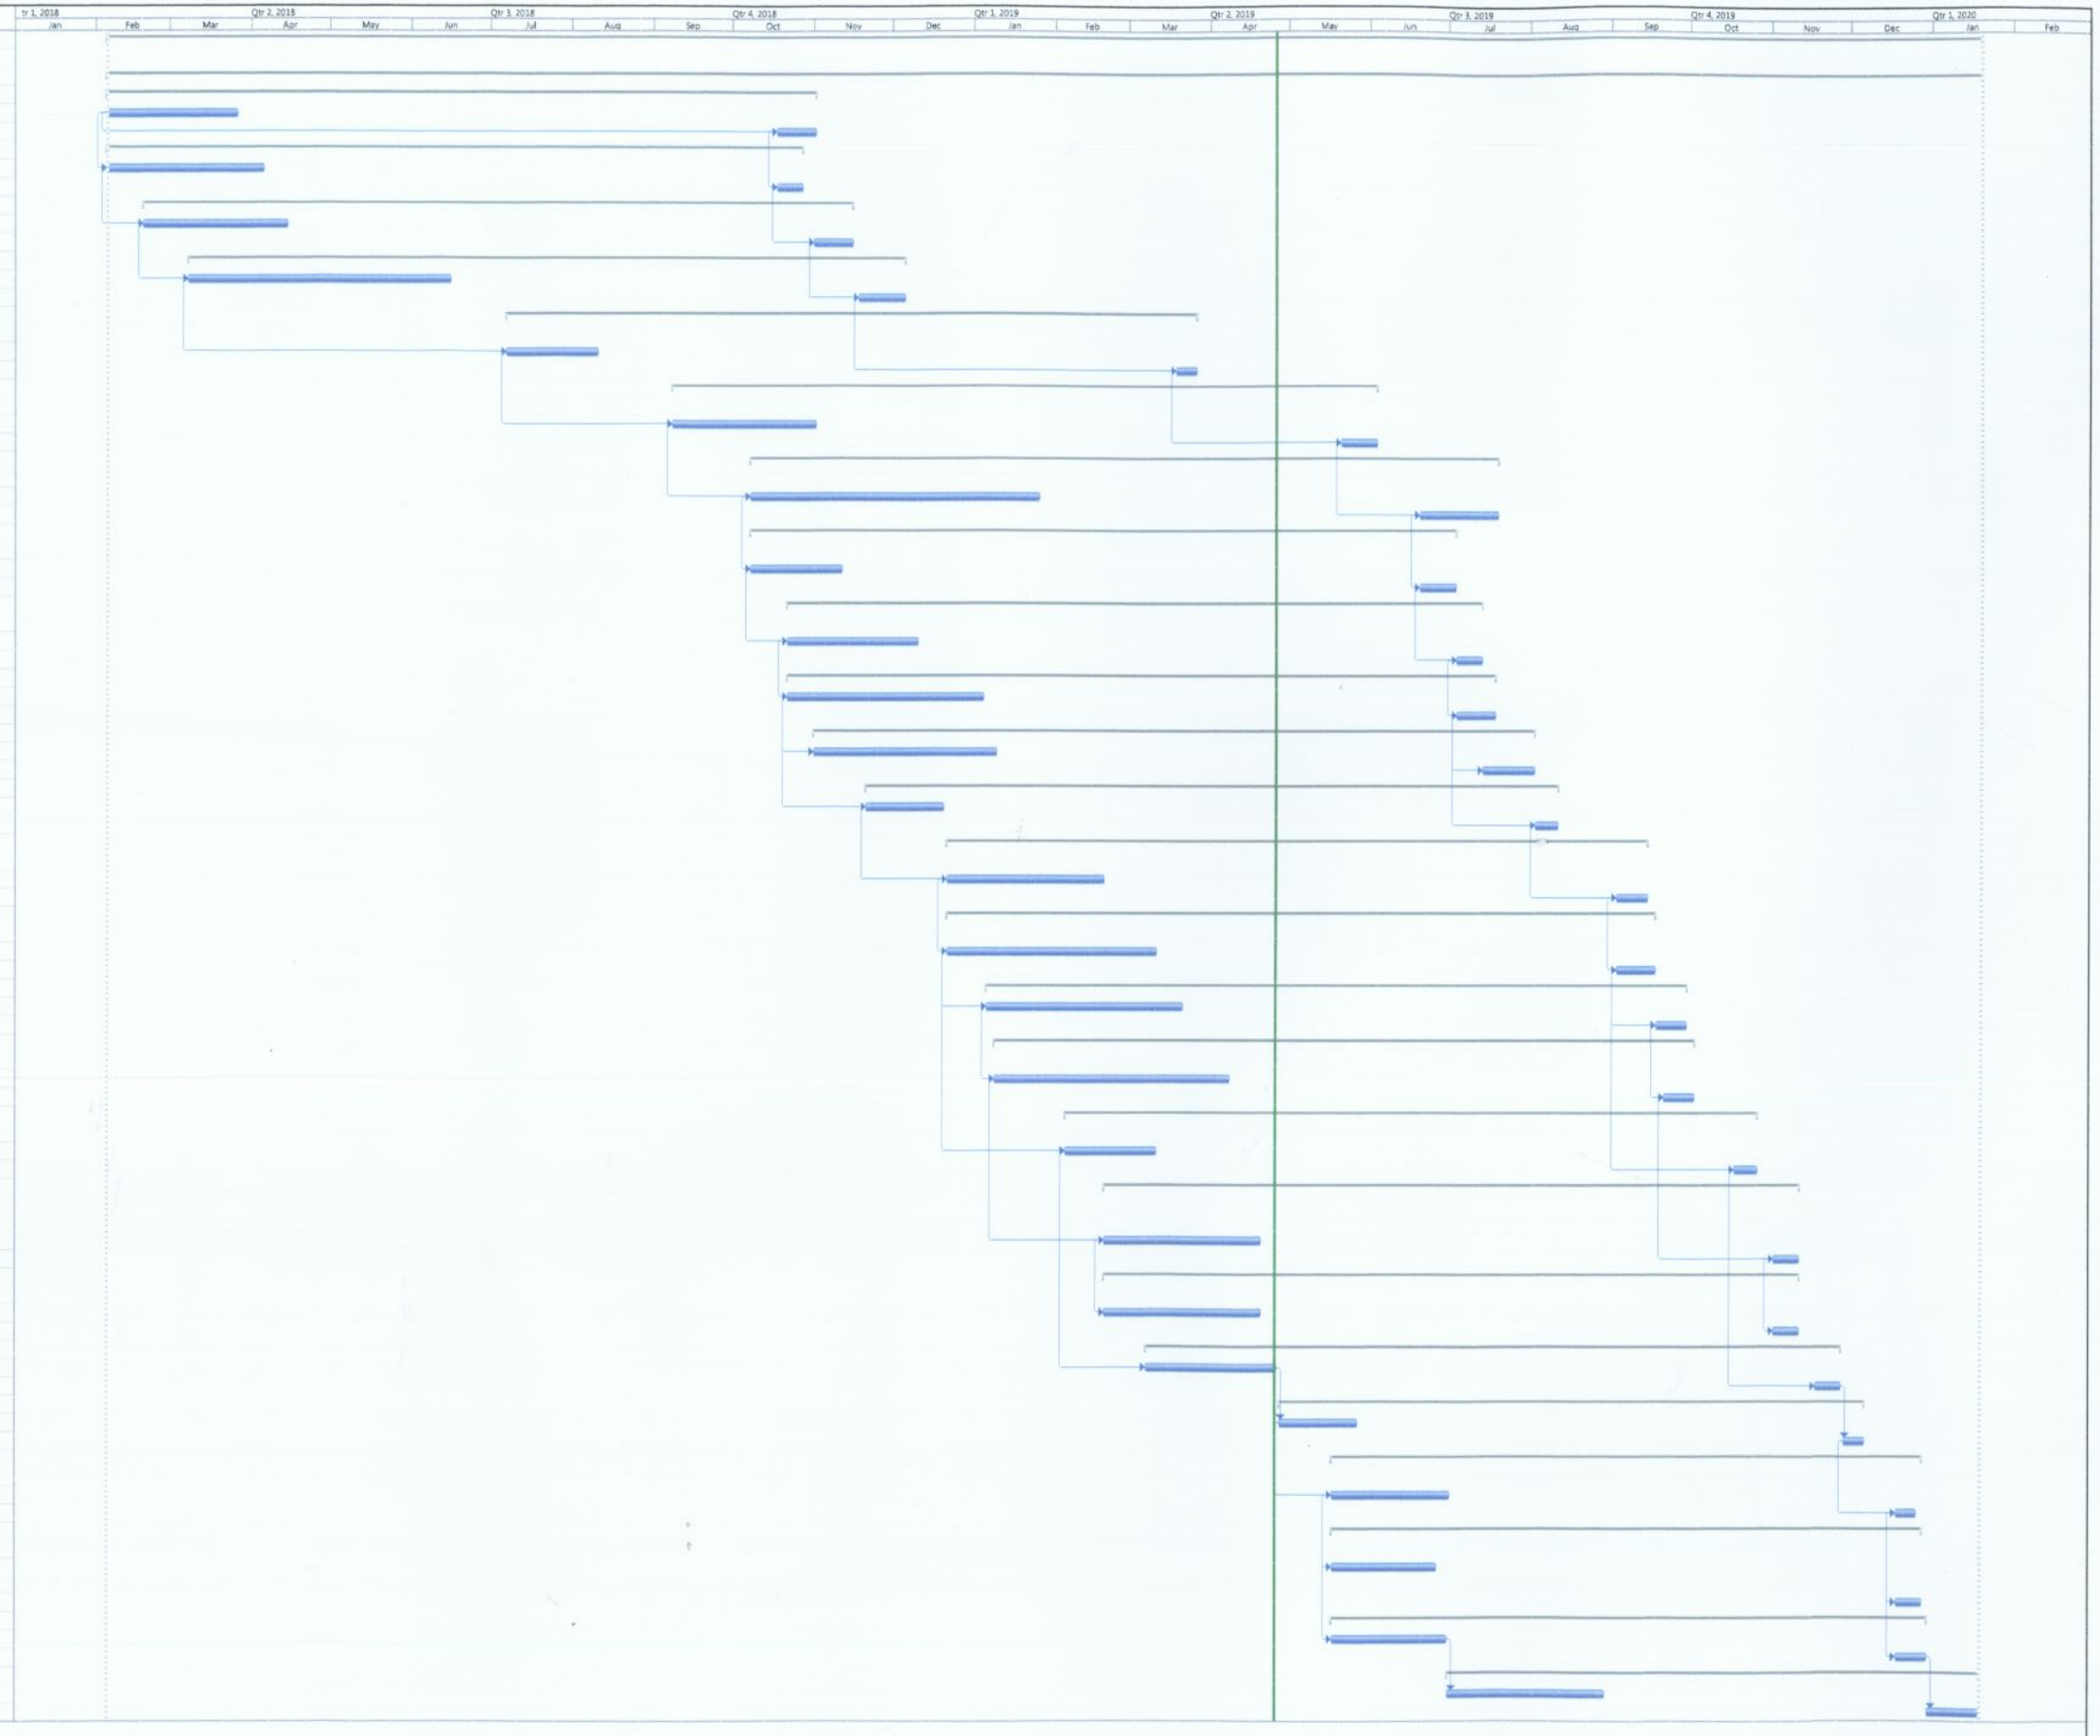

Project: EGV Debanshu Da
Date: Fri 26-04-19

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline | Progress
