Project : SOLACE - JOKA (G+III)

ID	Task Mode	Task Name	Duration	Start	Finish
1		**Project : Solace - Joka (G+III)**	**1390 days**	**Mon 21 May '18**	**Thu 22 Dec '22**
2		**Pre - Construction Activities :-**	**200 days**	**Mon 21 May '18**	**Wed 30 Jan '19**
3		Block Layout Drawing preparation	2 days	Mon 21 May '18	Tue 22 May '18
4		Civil Shop Drawing Preparation	10 days	Tue 22 May '18	Fri 01 Jun '18
5		Site Handover to Contractor	2 days	Fri 01 Jun '18	Mon 04 Jun '18
6		Site cleaning Activities	15 days	Mon 04 Jun '18	Mon 25 Jun '18
7		Earth dressing	10 days	Mon 25 Jun '18	Thu 05 Jul '18
8		Construction for Boudary Wall	30 days	Thu 05 Jul '18	Mon 06 Aug '18
9		Making of temporary drainage system	20 days	Mon 06 Aug '18	Mon 03 Sep '18
10		Construction of labour hutment	15 days	Mon 03 Sep '18	Thu 20 Sep '18
11		Prepartion of material yard	15 days	Thu 20 Sep '18	Wed 10 Oct '18
12		Shifting of ex.CESC meter room	15 days	Wed 10 Oct '18	Fri 09 Nov '18
13		Construction of Site office	25 days	Fri 09 Nov '18	Wed 12 Dec '18
14		Preparation of Site approch	30 days	Wed 12 Dec '18	Sat 12 Jan '19
15		Raw material vendor's finalization	7 days	Fri 18 Jan '19	Fri 25 Jan '19
16		Block layout drawing approval	2 days	Fri 25 Jan '19	Mon 28 Jan '19
17		Civil shop drawing approval	2 days	Tue 29 Jan '19	Wed 30 Jan '19
18					
19		**Construction Activities (Below EGL) :-**	**385 days**	**Tue 29 Jan '19**	**Wed 06 May '20**
20		Block layout	4 days	Tue 29 Jan '19	Fri 01 Feb '19
21		Foundation layout	15 days	Fri 01 Feb '19	Sat 16 Feb '19
22		TBM marking at site	4 days	Sat 16 Feb '19	Thu 21 Feb '19
23		Earth excavtion for foundation - Part-1	30 days	Sat 16 Feb '19	Mon 25 Mar '19
24		Earth excavtion for foundation - Part-2	30 days	Mon 25 Mar '19	Fri 26 Apr '19
25		Removal of dumping earth	15 days	Fri 26 Apr '19	Mon 13 May '19
26		Level checking	2 days	Mon 13 May '19	Wed 15 May '19
27		Shuttering - foundation	15 days	Wed 15 May '19	Thu 30 May '19
28		PCC - foundation	25 days	Thu 30 May '19	Mon 01 Jul '19
29		Reinforcement placing - foundation	25 days	Mon 01 Jul '19	Thu 01 Aug '19
30		Lavel & Center line checking by consultant	3 days	Thu 01 Aug '19	Sat 03 Aug '19
31		Consultant approval for casting	2 days	Sat 03 Aug '19	Tue 06 Aug '19
32		RCC concreting - Foundation	4 days	Tue 06 Aug '19	Sat 10 Aug '19
33		Rib beam casting	4 days	Sat 10 Aug '19	Tue 20 Aug '19
34		Curing Process	15 days	Tue 20 Aug '19	Thu 12 Sep '19
35		Column starter casting	20 days	Fri 13 Sep '19	Fri 18 Oct '19
36		Checking and approval from consultant	2 days	Fri 18 Oct '19	Mon 21 Oct '19
37		Reinforcement placing - Pedestal	15 days	Mon 21 Oct '19	Thu 14 Nov '19
38		Shuttering - Pedestal	15 days	Thu 14 Nov '19	Sat 30 Nov '19
39		RCC concreting - Pedestal	7 days	Sat 30 Nov '19	Sat 07 Dec '19
40		Curing Process	15 days	Sat 07 Dec '19	Mon 23 Dec '19
41		De-shuttering	10 days	Mon 23 Dec '19	Fri 03 Jan '20
42		250mm thk. Brick work upto Plinth level	20 days	Fri 03 Jan '20	Fri 24 Jan '20
43		Curing Process	15 days	Fri 24 Jan '20	Sat 08 Feb '20
44		Anti Termite Process	7 days	Sat 08 Feb '20	Sat 15 Feb '20
45		Back filling by earth	15 days	Mon 17 Feb '20	Tue 03 Mar '20
46		Compaction process	15 days	Tue 03 Mar '20	Fri 20 Mar '20
47		Costruction of UGR	20 days	Fri 20 Mar '20	Fri 10 Apr '20
48		Construction of Septic Tank	20 days	Fri 10 Apr '20	Wed 06 May '20
49					
50		**Ground Floor Activitise (RCC) :-**	**75 days**	**Wed 06 May '20**	**Sat 25 Jul '20**
51		Column casting	25 days	Wed 06 May '20	Mon 01 Jun '20
52		Lift well casting	15 days	Mon 01 Jun '20	Tue 16 Jun '20
53		Stair-case casting	15 days	Tue 16 Jun '20	Mon 06 Jul '20
54		GF roof casting	20 days	Mon 06 Jul '20	Sat 25 Jul '20
55					
56		**1st Floor Activitise (RCC) :-**	**75 days**	**Wed 05 Aug '20**	**Mon 09 Nov '20**
57		Column casting	25 days	Wed 05 Aug '20	Fri 04 Sep '20
58		Lift well casting	15 days	Sat 05 Sep '20	Tue 22 Sep '20
59		Stair-case casting	15 days	Tue 22 Sep '20	Thu 08 Oct '20
60		FF roof casting	20 days	Thu 08 Oct '20	Mon 09 Nov '20
61					
62		**2nd Floor Activitise (RCC) :-**	**75 days**	**Tue 01 Dec '20**	**Thu 18 Feb '21**
63		Column casting	25 days	Tue 01 Dec '20	Mon 28 Dec '20
64		Lift well casting	15 days	Mon 28 Dec '20	Tue 12 Jan '21
65		Stair-case casting	15 days	Tue 12 Jan '21	Fri 29 Jan '21
66		SF roof casting	20 days	Fri 29 Jan '21	Thu 18 Feb '21
67					
68		**3rd Floor Activitise (RCC) :-**	**75 days**	**Mon 01 Mar '21**	**Tue 01 Jun '21**
69		Column casting	25 days	Mon 01 Mar '21	Tue 30 Mar '21
70		Lift well casting	15 days	Tue 30 Mar '21	Sat 17 Apr '21
71		Stair-case casting	15 days	Sat 17 Apr '21	Tue 04 May '21
72		TF roof casting	20 days	Tue 04 May '21	Tue 01 Jun '21
73					
74		**Roof Top Activitise (RCC) :-**	**75 days**	**Fri 11 Jun '21**	**Fri 10 Sep '21**
75		Column casting	25 days	Fri 11 Jun '21	Wed 07 Jul '21
76		Lift machine room	15 days	Wed 07 Jul '21	Sat 31 Jul '21
77		Stair head room	15 days	Mon 02 Aug '21	Tue 17 Aug '21
78		Parapet Wall	20 days	Tue 17 Aug '21	Fri 10 Sep '21
79					
80		**Internal & External Finishing Work :-**	**330 days**	**Wed 17 Mar '21**	**Sat 09 Apr '22**
81		Grong Floor	60 days	Wed 17 Mar '21	Tue 01 Jun '21
82		1st Floor	60 days	Tue 01 Jun '21	Wed 11 Aug '21
83		2nd Floor	60 days	Wed 11 Aug '21	Wed 20 Oct '21
84		3rd Floor	60 days	Wed 20 Oct '21	Sat 01 Jan '22
85		Roof Top	50 days	Sat 01 Jan '22	Wed 23 Feb '22
86		Parking & Open Space Area	40 days	Thu 24 Feb '22	Sat 09 Apr '22
87					
88		**Main Gate, Landscapping & Others activities :-**	**200 days**	**Fri 22 Apr '22**	**Thu 22 Dec '22**
89		Main gate	25 days	Fri 22 Apr '22	Wed 25 May '22
90		Landscapping	30 days	Thu 26 May '22	Sat 25 Jun '22
91		Drainage system	30 days	Sat 25 Jun '22	Fri 29 Jul '22
92		Lift Installation & Commissioning	30 days	Fri 08 Jul '22	Thu 11 Aug '22
93		Water Line connection	30 days	Thu 11 Aug '22	Mon 12 Sep '22
94		Roof Top Solar System installation	45 days	Mon 12 Sep '22	Mon 21 Nov '22
95		Site Visit / Joint Inspection	5 days	Mon 21 Nov '22	Sat 26 Nov '22
96		Final Rectification	20 days	Sat 26 Nov '22	Sat 17 Dec '22
97		Final Joint Site Inspection	3 days	Sat 17 Dec '22	Tue 20 Dec '22
98		Project Hand over	2 days	Tue 20 Dec '22	Thu 22 Dec '22

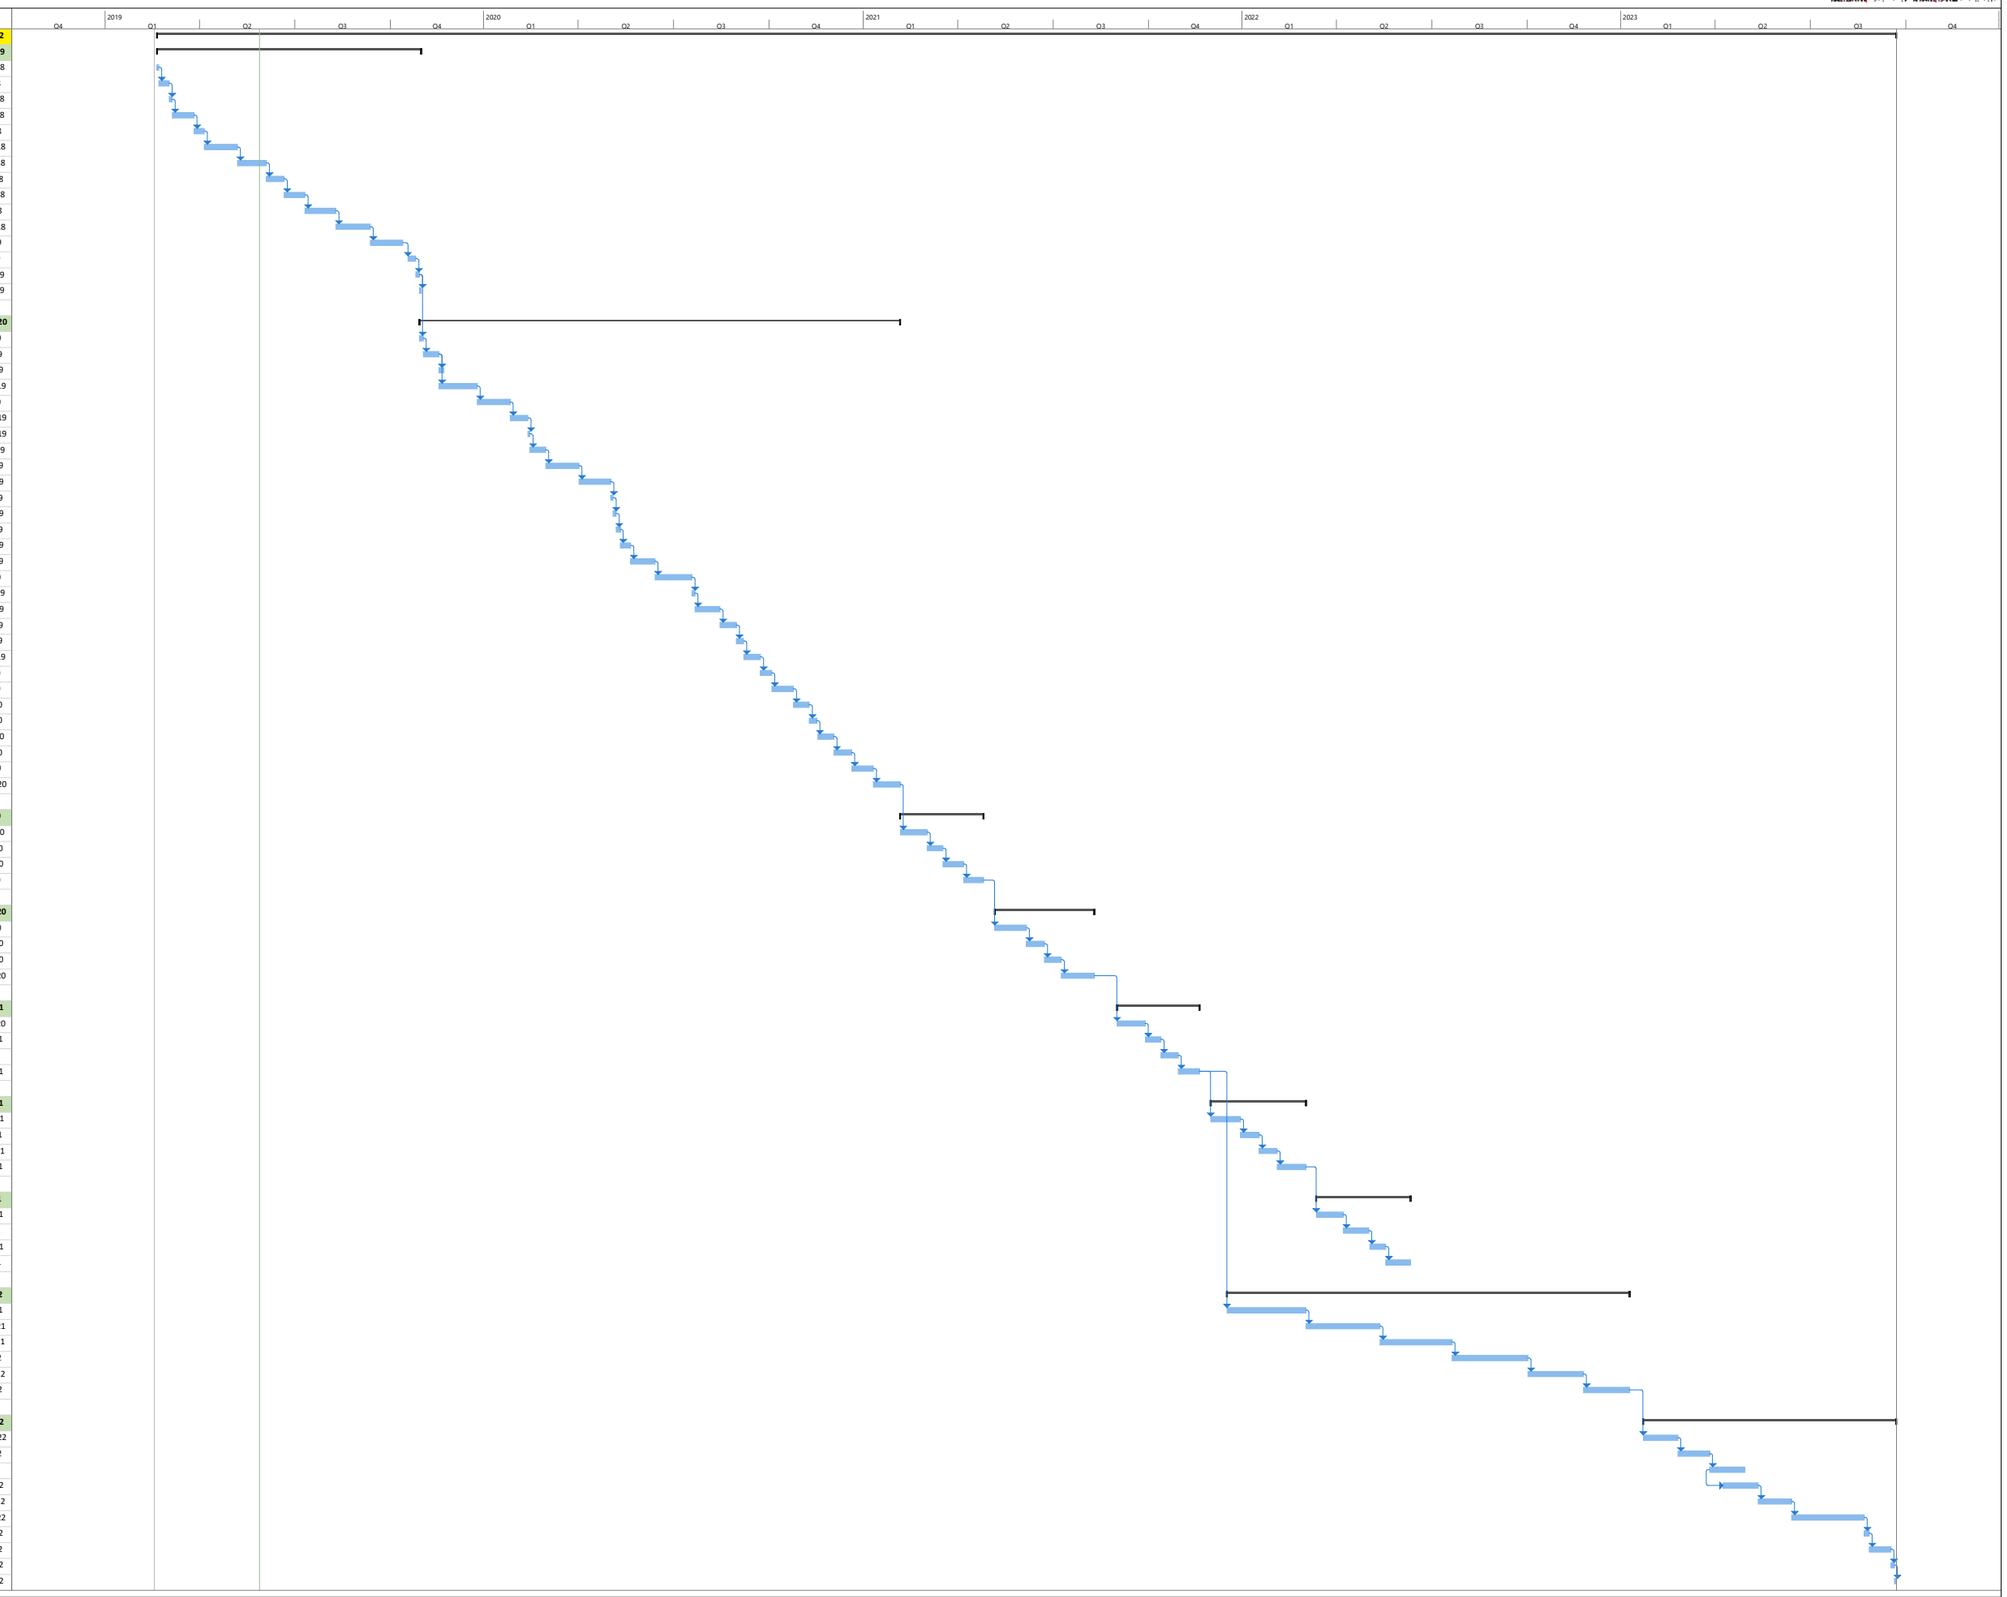

Project: SOLACE Joka Project
Date: Tue 28 Aug '18

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
