Project : SOLARIS PHASE - II (G+12 & G+13)

edenREALTY
Building Dreams. Designing Lifestyle

ID	Task Mode	Task Name	Duration	Start	Finish
1		**Project : Solaris Phase - II (G+12 & G+13), Tower - 3 & 4**	**982 days**	**Mon 28 May '18**	**Tue 31 Aug '21**
2		**Pre - Construction Activities :-**	**97 days**	**Mon 28 May '18**	**Thu 20 Sep '18**
3		Test Pile Activities	45 days	Mon 28 May '18	Wed 18 Jul '18
4		Site cleaning Activities	15 days	Thu 05 Jul '18	Fri 20 Jul '18
5		Reparing of Boudary Wall	30 days	Fri 20 Jul '18	Tue 28 Aug '18
6		Making of temporary drainage system & water Tank	20 days	Fri 17 Aug '18	Wed 12 Sep '18
7		Construction of labour hutment	20 days	Fri 17 Aug '18	Wed 12 Sep '18
8		Making of temporary front Gate no.1 & 2	20 days	Tue 28 Aug '18	Thu 20 Sep '18
9		Demolition of existing structure & removal of debris	30 days	Thu 28 Jun '18	Sat 28 Jul '18
10		Construction of Site office	20 days	Mon 30 Jul '18	Mon 27 Aug '18
11		Material & Labour vendor's finalization	10 days	Thu 09 Aug '18	Mon 27 Aug '18
12		**Construction Activities (Below EGL) :-**	**203 days**	**Sat 28 Jul '18**	**Fri 12 Apr '19**
13		Construction of Pile Foundation (500 dia) activities with testing	75 days	Sat 28 Jul '18	Mon 19 Nov '18
14		Pile Cap Layout for both tower	10 days	Sat 03 Nov '18	Fri 23 Nov '18
15		Earth excavtion for foundation & TB	60 days	Sat 03 Nov '18	Mon 21 Jan '19
16		Pile cap & tie beam casting activities	65 days	Mon 10 Dec '18	Fri 22 Feb '19
17		Anti Termite Process	20 days	Tue 05 Feb '19	Mon 25 Feb '19
18		Column starter casting	25 days	Sat 02 Mar '19	Tue 02 Apr '19
19		Back filling activities	25 days	Wed 13 Mar '19	Fri 12 Apr '19
20		UGR costruction activities	45 days	Thu 14 Feb '19	Fri 05 Apr '19
21		**RCC Slab Casting (Incl. Stair, Lift well, Col.)**	**422 days**	**Mon 18 Mar '19**	**Tue 04 Aug '20**
22		GR Floor	30 days	Mon 18 Mar '19	Wed 24 Apr '19
23		1st Floor	30 days	Mon 22 Apr '19	Fri 24 May '19
24		2nd Floor	30 days	Wed 22 May '19	Thu 27 Jun '19
25		3rd Floor	30 days	Wed 26 Jun '19	Wed 31 Jul '19
26		4th Floor	30 days	Tue 30 Jul '19	Thu 12 Sep '19
27		5th Floor	30 days	Wed 11 Sep '19	Sat 26 Oct '19
28		6th Floor	30 days	Thu 24 Oct '19	Wed 04 Dec '19
29		7th Floor	30 days	Mon 02 Dec '19	Fri 03 Jan '20
30		8th Floor	30 days	Wed 01 Jan '20	Sat 01 Feb '20
31		9th Floor	30 days	Thu 30 Jan '20	Mon 02 Mar '20
32		10th Floor	30 days	Fri 28 Feb '20	Thu 02 Apr '20
33		11th Floor	30 days	Tue 31 Mar '20	Tue 05 May '20
34		12th Floor	30 days	Mon 04 May '20	Wed 03 Jun '20
35		13th Floor	30 days	Tue 02 Jun '20	Mon 06 Jul '20
36		Roof Top	30 days	Sat 04 Jul '20	Tue 04 Aug '20
37					
38		**Internal & External Finishing Work :-**	**480 days**	**Fri 28 Jun '19**	**Mon 01 Feb '21**
39		Grong Floor	60 days	Fri 28 Jun '19	Thu 19 Sep '19
40		1st Floor	60 days	Fri 02 Aug '19	Mon 11 Nov '19
41		2nd Floor	60 days	Thu 19 Sep '19	Thu 12 Dec '19
42		3rd Floor	60 days	Tue 12 Nov '19	Tue 14 Jan '20
43		4th Floor	60 days	Thu 12 Dec '19	Thu 13 Feb '20
44		5th Floor	60 days	Tue 14 Jan '20	Wed 18 Mar '20
45		6th Floor	60 days	Fri 14 Feb '20	Wed 22 Apr '20
46		7th Floor	60 days	Wed 18 Mar '20	Sat 23 May '20
47		8th Floor	60 days	Wed 22 Apr '20	Sat 27 Jun '20
48		9th Floor	60 days	Mon 25 May '20	Wed 29 Jul '20
49		10th Floor	60 days	Sat 27 Jun '20	Wed 02 Sep '20
50		11th Floor	60 days	Wed 29 Jul '20	Tue 06 Oct '20
51		12th Floor	60 days	Thu 03 Sep '20	Sat 28 Nov '20
52		13th Floor	60 days	Tue 06 Oct '20	Wed 30 Dec '20
53		Roof Top	60 days	Sat 28 Nov '20	Mon 01 Feb '21
54		**Post Construction & Miscellaneous Activities :-**	**358 days**	**Sat 27 Jun '20**	**Tue 31 Aug '21**
55		Construction of main gate	30 days	Mon 01 Feb '21	Thu 04 Mar '21
56		Lift Installation & Commissioning	90 days	Sat 28 Nov '20	Thu 04 Mar '21
57		Construction of STP & WTP	90 days	Sat 27 Jun '20	Tue 06 Oct '20
58		Water & Sewer Line connection	30 days	Thu 04 Mar '21	Tue 06 Apr '21
59		Roof Top Solar System Installation	45 days	Thu 04 Mar '21	Mon 26 Apr '21
60		Fire Fighting instruments Installation	90 days	Wed 27 Jan '21	Fri 07 May '21
61		Landscapping & Boundary Wall	90 days	Wed 07 Apr '21	Thu 29 Jul '21
62		Site Visit / Joint Inspection	4 days	Fri 30 Jul '21	Tue 03 Aug '21
63		Rectification + Final Joint Site Inspection	22 days	Tue 03 Aug '21	Mon 30 Aug '21
64		Project Hand over	2 days	Mon 30 Aug '21	Tue 31 Aug '21

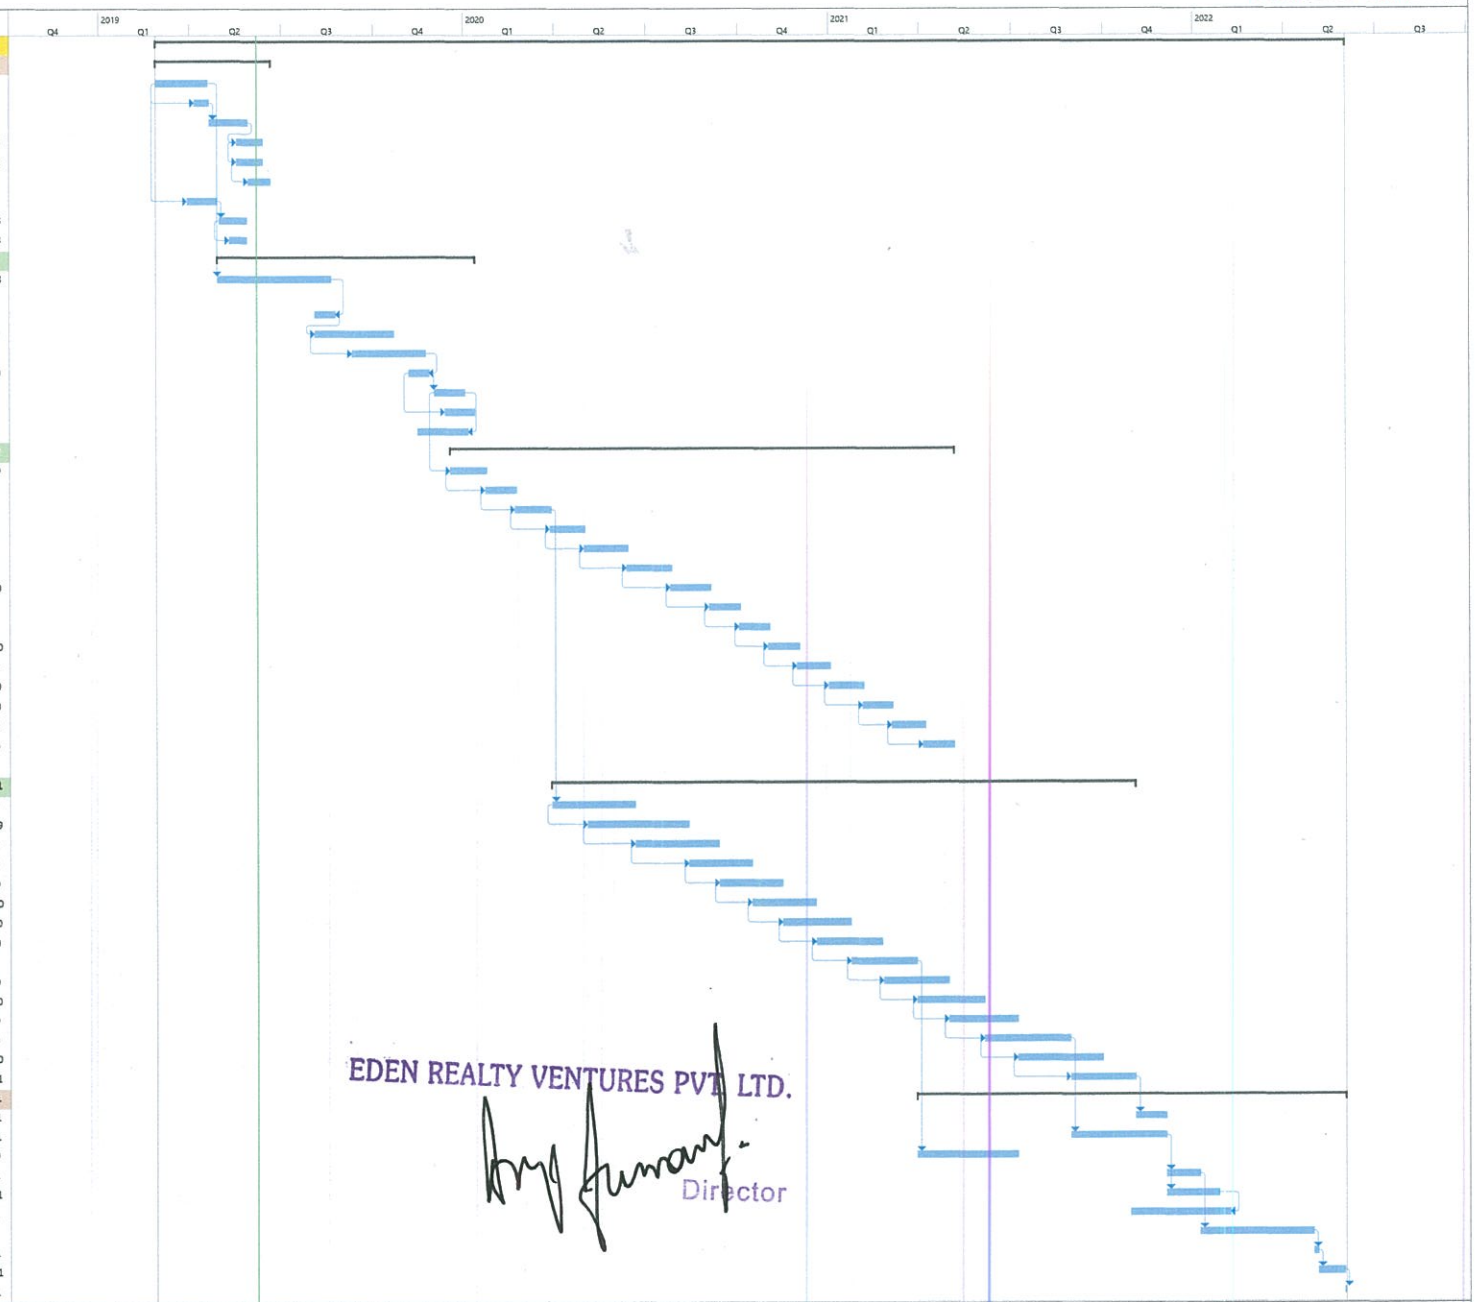

EDEN REALTY VENTURES PVT. LTD.
Director

Project: SOLACE Joka Project
Date: Thu 06 Sep '18

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
