SIDDHA ESPLANADE

GRNTT CHART
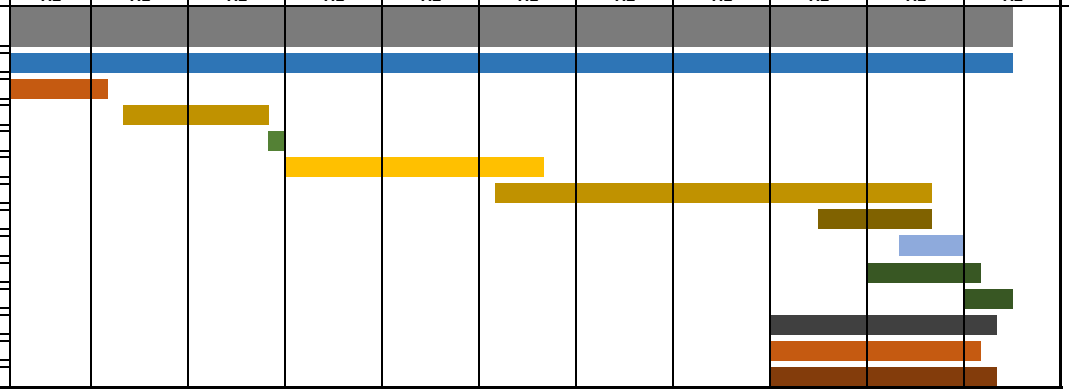
SL No.	Task Name	Start	Finish	Duration (Days)
	SIDDHA ESPLANADE PROJECT B+G+17 01 NOS BUILDING, MLCP.	18-Aug-15	30-Sep-20	1870
1	MAIN BUILDING - B+ G+17	18-Aug-15	30-Sep-20	1870
	PILING	18-Aug-15	1-Feb-16	167
	SUB STRUCTURE	13-Mar-16	30-Nov-16	262
	GR. FLOOR ROOF	1-Dec-16	3-Jan-17	33
	1st FLOOR ROOF TO 17th FLOOR ROOF	4-Jan-17	8-Apr-18	459
	FINISHING	1-Feb-18	30-Apr-20	819
	SERVICES	1-Oct-19	30-Apr-20	212
	GR. FLOOR LOBBY & PARKING	1-Mar-20	30-Jun-20	121
	SNAGGING & DESNAGGING	1-Jan-20	31-Jul-20	212
	FLAT HANDOVER	1-Jul-20	30-Sep-20	91
2	COMMON DEVELOPMENT	1-Jul-19	31-Aug-20	427
	MLCP	1-Jul-19	31-Jul-20	396
	INFRASTRUCTURE	1-Jul-19	31-Aug-20	427
