ID	Task Name	Duration	Start	Finish
1	**PLANNED - WORK SCHEDULE (IDEAL ROYALE)**	**1787 days**	**14-01-16**	**31-12-21**
2	**BUILDING WORKS**	**1787 days**	**14-01-16**	**31-12-21**
3	PRELIMINARY WORKS	45 days	14-01-16	05-03-16
4	**TOWER (G+23)**	**1674 days**	**07-03-16**	**02-10-21**
5	PILING WORK	337 days	07-03-16	06-04-17
6	EXCAVATION AND SHORING WORK	209 days	07-04-17	22-12-17
7	BFS & PCC WORK	45 days	08-06-17	29-07-17
8	**RCC STRUCTURE WORK**	**556 days**	**16-06-17**	**04-05-19**
9	SUB-STRUCTURE WORK	106 days	16-06-17	31-10-17
10	SUPER STRUCTURE WORK	501 days	21-08-17	04-05-19
11	BRICK WORK & PLASTER WORK	810 days	10-05-18	01-02-21
12	WATERPROOFING WORK	765 days	16-12-17	08-07-20
13	FLOORING	390 days	05-02-20	26-05-21
14	WOOD WORKS (INC. JOINERY WORKS)	390 days	13-03-20	30-06-21
15	ALUMINUM & GLAZING WORKS	393 days	21-03-20	12-07-21
16	RAILING, GRILL, MS WORKS	327 days	25-04-20	29-05-21
17	FAÇADE WORKS	201 days	27-08-20	05-05-21
18	PAINTING WORKS	396 days	12-02-20	09-06-21
19	FALSE CEILING	172 days	12-08-20	15-03-21
20	LIFT	150 days	01-09-20	08-03-21
21	SANITARY AND PLUMBING WORKS	795 days	07-02-19	02-10-21
22	ELECTRICAL WORKS	1170 days	12-10-17	09-09-21
23	FIRE FIGHTING WORKS & PA SYSTEM	250 days	10-06-20	13-04-21
24	PRESSURIZATION WORKS (STAIRCASE & LIFT LOBBY)	135 days	26-08-20	12-02-21
25	AIR CONDITIONING WORKS	195 days	10-11-20	30-06-21
26	CCTV & EPABX	27 days	21-05-21	21-06-21
27	**COMMUNITY HALL & GYM**	**270 days**	**10-10-20**	**04-09-21**
28	BOUNDARY WALL, SECURITY CABIN, MAIN GATE	1030 days	02-11-17	17-04-21
29	UNDERGROUND WATER RESERVOIR, PUMP ROOM, RWH PIT	600 days	30-08-18	05-09-20
30	INTERNAL ROAD & PARKING AREA	595 days	16-05-19	14-05-21
31	CABLE TRENCH, TRANSFORMER, METER PANEL, DG	778 days	10-04-19	22-11-21
32	MLCP	120 days	28-07-21	27-12-21
33	LANDSCAPE	677 days	19-09-19	31-12-21

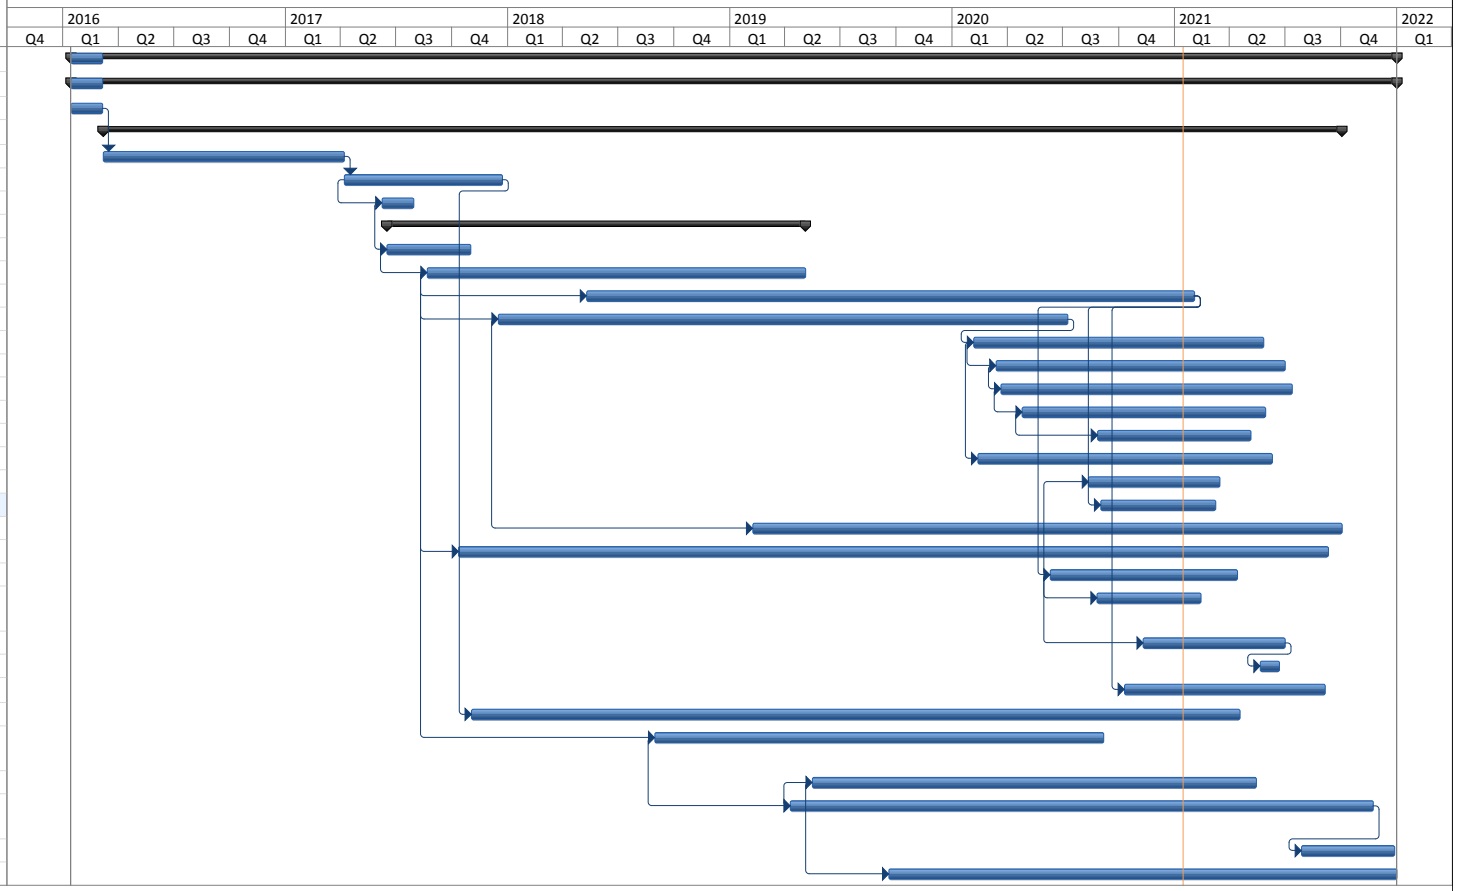

Project: msproj11
Date: 15-01-21

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline	
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress	
